Deh. 859

Standard Form No. 1034
7 GAO 5030
1034-107

PUBLIC VOUCHER FOR PURCHASES AND SERVICES OTHER THAN PERSONAL

Use continuation sheet(s) if necessary

VOU. NO. _____

BU. VOU. NO. 2592

U. S. Department of the Interior - Office of the Secretary
(Department, bureau, or establishment)

Voucher prepared at _____
(Give place and date)

Payee's Account No. _____ Discount Terms _____

TO The Baltimore Syndicate, Ltd.
(Payee)

P. O. Box 755, Heppner, Oregon
(Address)

PAID BY

Contract No. _____ Date _____ Req. No. _____ Date _____ Invoice Rec'd. _____

Shipped from _____ to _____ Weight _____ Govt. B/L No. _____

No. and Date of Order	Date of Delivery or Service	ARTICLES OR SERVICES (Enter description, item number of contract or Federal supply schedule, and other information deemed necessary)	Quantity	UNIT PRICE Cost	UNIT PRICE Per	AMOUNT *
2102		Final payment per Report of Review dated 11/28/60				
Reg. I		See supporting documents in contract file				
		Contract holdback 100.00				102.50
		Add. allowance 2.50				
			TOTAL			102.50

OFFICIAL FILE COPY
O. M. E
RECEIVED DEC 21 1960

DATE	INITIALS	CODE
12/24	Cae	210
		1104
PAYMENT:		500
COMPLETE ☐		
PARTIAL ☐		
FINAL ☐		
PROGRESS ☐		
ADVANCE ☐		

(PAYEE MUST **NOT** USE THIS SPACE)

DIFFERENCES _____

Amount verified; correct for 102.50
(Signature or initials) _____

† Approved for _____ =$ 102150
By _____
Title _____
Exchange rate _____ =$1.00

Pursuant to authority vested in me, I certify that this voucher is correct and proper for payment.

† _____
(Authorized Certifying Officer) (Date)

THE REVERSE OF THIS FORM MUST BE EXECUTED WHEN PURCHASES ARE MADE OR SERVICES SECURED WITHOUT WRITTEN AGREEMENT IN ANY FORM

ACCOUNTING CLASSIFICATION (Appropriation Symbol must be shown; other classification optional)

14X6875(01) Suspense, Department of the Interior 100.00

14X0108 Salaries and Expenses, Office of Min. Exp. 2.50

501 (60) 2.50 2.50

Paid by
Check No. _____ on Treasurer of the United States
Check No. _____ on _____ (Name of Bank)
Cash, $ _____, on _____, 19____ Payee _____

Per _____

Title _____

* When used in foreign countries, insert name of currency of country in which used.

† If the ability to certify and authority to approve are combined in one person, one signature only is necessary; otherwise the approving officer will sign on the line below "Approved for $ _____", and over his official title.

METHOD OF OR ABSENCE OF ADVERTISING

METHOD OF ADVERTISING

1. Advertising in newspapers Yes ☐ No ☐.
2. (*a*) Advertising by circular letters sent to ..... dealers.
   (*b*) And by notices posted in public places Yes ☐ No ☐.

   (If notices were not posted in addition to advertising by circular letters sent to dealers, explanation of such omission must be made below.)

ABSENCE OF ADVERTISING

3. Without advertising, under an exigency of the service which existed prior to the order and would not admit of the delay incident to advertising.
4. Without advertising in accordance with .....
5. Without advertising, it being impracticable to secure competition because of .....

.....

.....

.....

.....

(Here state in detail the nature of the exigency or circumstances under which the securing of competition was impracticable under 3 and 4)

NOTE.—The above form "Method of or Absence of Advertising" is to be used when purchases are made or services secured under proper authority without written agreement in any form. In case of a written agreement (formal contract, proposal, and acceptance, or less formal agreement) Standard Form No. 1036 should be used for abstracting the method of or absence of advertising and award of contract. (See 7 GAO 4500 and 5000.)

☆ U.S. GOVERNMENT PRINTING OFFICE: 1959 O—513814

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION
So. 157 Howard Street
Spokane 4, Washington
April 8, 1960

OFFICIAL FILE COPY
O. M. E.
RECEIVED APR 11 1960

DATE	INITIALS	CODE
4-11	gad	2 N 0
"	[illegible]	110
4/12	[illegible]	800
	[illegible]	500

Memorandum

To: Chairman, Operating Committee, OME

From: Executive Officer, OME Field Team, Region I

Subject: Transmittal of inspection report

Enclosed are the original and two copies of the following interim inspection report:

OME		Date
6045	Baltimore Syndicate, Ltd., Baltimore mine, Jefferson County, Montana	4/ 8/60

D. R. MacLaren
For: A. E. Weissenborn

Enclosure

OFFICIAL FILE COPY
O. M. E.
RECEIVED APR 11 1960

DATE	INITIALS	CODE
4-11	gard	VVO
		110
		800
		500

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION
So. 157 Howard Street
Spokane 4, Washington
April 8, 1960

Memorandum

To: OME Field Team, Region I

From: R. D. Sample, Geologist, U. S. Geological Survey

Subject: Interim inspection report, Docket No. OME-6045 (lead-zinc-copper), Baltimore Syndicate, Ltd., Baltimore Mine, Jefferson County, Montana, Contract No. 14-23-090-2102

A visit was made to Jefferson City, Montana, on March 24, 1960, to inspect and log the core from the diamond drilling project at the Baltimore mine. The core is stored at the home of Louis Peura's mother. Mr. Peura, manager of the mine, was present at the time of inspection. The last inspection was made by S. W. Zoldok, Engineer, Bureau of Mines, on December 2, 1959.

Only the stored core was examined and logged as the road to the mine was inaccessible and an examination of the mine was impossible at the time of the visit.

A total of 1,202 feet of core was examined which represented core from Holes No. 1-6, inclusive. Hole No. 4 was completed from 121 feet to 198 feet and Holes No. 5 and 6 were drilled to 196 feet and 195 feet 10 inches, respectively, since Mr. Zoldok's visit in December. Core recovery was good with approximately 90 percent recovery. All of the drilling was through altered, quartz-monzonite country rock or through massive, fractured quartz veins. Most of the quartz veins showed some flecks or small blebs of iron, copper, or copper sulfides scattered over wide areas, here and there larger blebs in the shattered zones but only for a few inches. Four samples (pl. 1) were taken by the Operator which showed weak mineralization. Some samples of the dark-colored quartz were taken by Zoldok and tested for tungsten. These proved to be chemically altered stringers of bornite. None of the samples assayed gave promise for a commercial ore shoot.

Upon completion of the six diamond drill holes with 1,202 feet of drilling, Stage I of the project contract has been completed. This first stage was unsuccessful in locating an attractive target area for crosscutting as outlined in Stage II. Mr. Peura expressed a desire to crosscut southwesterly from the No. 2, 3, and 4 drill

sites where all three holes intersected a slightly mineralized zone at about 20-30 feet (pl. 1). However, this view is not held by the examiner, and it is recommended that Stage II not be authorized.

Status of contract

Stage I

Date of contract: July 27, 1959
Termination date: January 27, 1961
Amount of contract: $22,930.00
Amount spent: $ 7,514.00 (thru Dec. 1959)

Item	Authorized	Completed
Mobilization and Demobilization	$150.00	Yes
Diamond drilling	1200 ft	1202 ft 1/
Reaming, casing, etc.	300 ft	80 ft
Core boxes	40	28
Assaying	200 determinations	22
Rehab. Hope Tunnel	$750.00	Yes
Repair comp. house	$150.00	No
Incidental allowance	1200 ft	1200 ft
Diamond drill stations	2	2

1/ Hole 1 - 205'
2 - 207'
3 - 200'2"
4 - 198'
5 - 196'
6 - 195'10"

Stage II - not started

R. D. Sample

Enclosure (pl. 1)
Distribution:
(OME 3)
(USBM 2)
(Docket)
(Sample)

(This interim inspection report was written by RDS on March 29 and typed April 8.)

UNITED STATES
DEPARTMENT OF THE INTERIOR

PREPARED FOR
OFFICE OF MINERALS EXPLORATION
INTERIM REPORT

DOCKET NO. OME 6045 (Lead-Zinc-Copper)

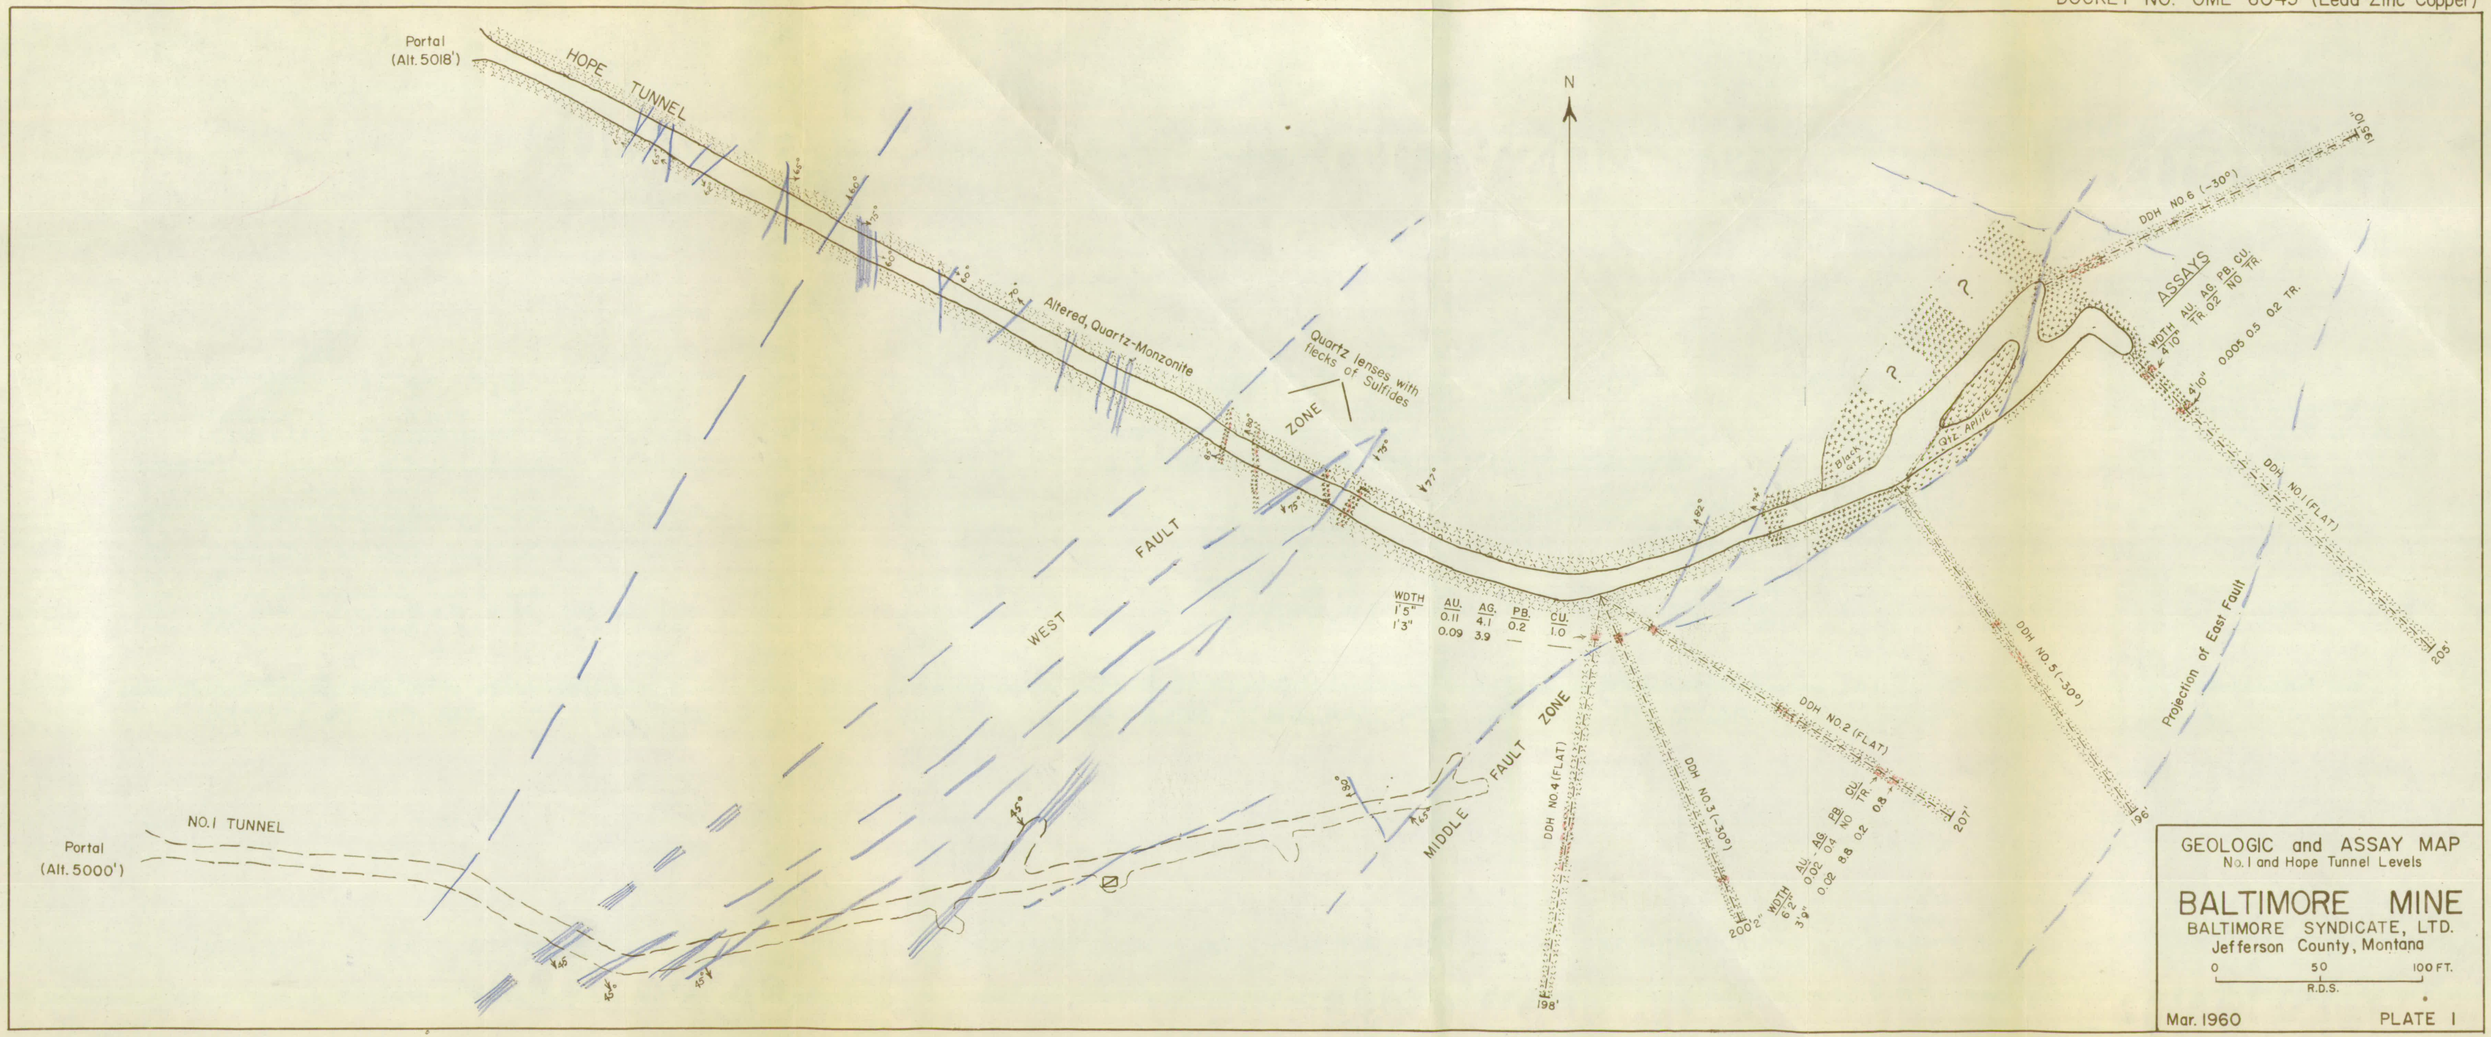

GEOLOGIC and ASSAY MAP
No. 1 and Hope Tunnel Levels

BALTIMORE MINE
BALTIMORE SYNDICATE, LTD.
Jefferson County, Montana

0 50 100 FT.
R.D.S.

Mar. 1960 PLATE 1

Baltimore Mine Docket No. 6045 Narrative

Stage one of this Contract is completed and we are now in favor of beginning Stage two. unfortunately three of the D.D. holes were for a large part in faults however from a study of the cores we believe sufficient information can be had to plot some of the ore occurrences.

Inclement weather delayed drilling until Feb at the present time snow is rather deep at the mine but the cores are at Jeff. City ready for inspection, perhaps one sample can come over and log and study them, we will cooperate with him.

MME FORM 60
SEPT. 1959

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION

MAR 25 1960

Docket No. 1439
Contract No. 6045
O.M.E. 14-23-090 2102
Contract Amount $ 22,930.00
Gov't. Participation % 50 $ 11,465.00
Mineral(s) Cu. Pb.Zn.

OPERATOR'S MONTHLY VOUCHER

For Month of Feb. 1960

Operator's Name Baltimore Syndicate Ltd.
Address P.O. Box 755 Heppner, Oregon

COST CATEGORIES	FOR OPERATOR'S USE			FOR GOVERNMENT APPROVAL ONLY		
	MONTHLY TOTAL	PREVIOUSLY REPORTED	TOTALS TO DATE	MONTHLY TOTAL	PREVIOUSLY REPORTED	TOTALS TO DATE
Fixed Unit Costs and						
(1) Independent Contracts:						
Building Drill Sta.	0	400.00	400.00		400.00	400.00
Rehab. Hppe	0	750.00	750.00		750.00	750.00
Mobil & Demob.	0	150.00	150.00		150.00	150.00
Drilling Core	1020.00	5100.00	6120.00	1020.00	5100.00	6120.00
Over reaming	240.00	.00	240.00	180.00	—	180.00
Incidental Allow	200.00	1000.00	1200.00	200.00	1000.00	1200.00
(2) Personal Services:						
Supervision & Technical						
Outside Consultants						
Labor						
(3) Operating Mat'l. & Supplies:						
Timber						
Explosives						
Pipe						
Rail						
Core boxes	20.00	92.00	112.00	20.00	92.00	112.00
(4) Operating Equipment:						
Rental						
Purchase						
Depreciation						
(5) Initial Rehab. & Repairs:						
Buildings, Fixtures, etc.						
Operating Equipment						
(6) New Buildings, Fixtures, etc.						
(7) Miscellaneous:						
Repairs to Equipment						
Analytical Work Assays	0	27.00	27.00	—	22.00	22.00
Payroll Taxes						
Employee's Liability Ins.						
TOTALS	1480.00	7519.00	8999.00	1420.00	7514.00	8,934.00

I certify that the above bill is correct and just and that payment therefor has not been received.

Date 3/2/60 *Payee Baltimore Syndicate Ltd.

Per C.M. Wagner Title General Partner

* When a voucher is signed or receipted in the name of a company or corporation, the name of the person writing the company or corporate name, as well as the capacity in which he signs, must appear. For example: "John Doe Company, per John Smith, Secretary," or "Treasurer," as the case may be.

A willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction is a criminal offense. (U.S. Code, Title 18, Sec. 1001.)

(INSTRUCTIONS ON REVERSE)

Pursuant to authority vested in me, I certify that this account is correct and proper for payment in the amount of: 610.00 to Operator
100.00 to Suspense (holdback)

$

Signature
(Authorized Certifying Officer)

Date Vou. No.

(SEE OTHER SIDE)

Certification by Government Representative:

I certify that to the best of my knowledge and belief the contractor submitting this voucher is operating an exploration project in accordance with the terms of Contract No. _____

Signature _____ Title _____ Date _____

Approved by OME Executive Officer or Alternate:

Signature _____ Title _____ Date _____

OPERATOR'S MONTHLY REPORT

The Operator, under an Office of Minerals Exploration contract, is required to report monthly to the Government. The report consists of three parts.

FIRST, the Operator's Monthly Voucher on MME Form 60 listing the project costs incurred and claimed by the Operator is the voucher basis for payment of the Government's share of the cost.

SECOND, the Operator's Progress Report on MME Form 61 is a statistical report of the units and cost of of work performed under the contract.

THIRD, the Operator's Narrative Report is a concise description of the work performed, results accomplished, and any unusual situations encountered, illustrated and supported by engineering-geological maps or sketches, drill hole logs, assay reports, etc., as pertinent.

The Operator submits the original and four copies of each of the three sections of this report to the OME regional Executive Officer at the end of each month during the life of the contract.

PREPARATION OF OPERATOR'S MONTHLY VOUCHER, MME FORM 60

After all applicable spaces are filled in, the Operator or his agent must sign the certification in the lower left corner. Categories (2) through (7) apply to "Actual Cost" contracts only.

Under "Fixed Unit Costs" and Category (1) report, (a) the total fixed unit costs of work performed under contract provisions for contribution by the Government on a basis of "fixed unit costs"; and (b) the claimed costs of work performed on a unit-price basis by independent contractors.

Under Category (2) include the claimed costs of all payrolled and invoiced supervisory, technical, and labor personnel, except the costs for services applicable to Categories (5) and (6).

Under Category (3) include the claimed costs of all project materials and supplies other than those used for work under Categories (5) and (6).

Under Category (4) report claimed rentals on equipment belonging to a third party, claimed payments or obligations for payments on the Operator's purchase of equipment, and claimed depreciation for the use of Operator-owned equipment.

Under Categories (5) and (6) include all claimed costs of labor, supervision, technical services, operating materials and supplies, and all other items used in (5) the initial rehabilitation and repairs of existing buildings, fixtures, installations (exclusive of mine workings), and operating equipment; and (6) the installation or construction of new buildings, fixtures, and fixed improvements (exclusive of mine workings). Do not report these costs under Categories (2), (3), (4), and (7).

Under Category (7) include all miscellaneous claimed costs such as repairs (other than initial) and maintenance of equipment, sampling and analysis, travel, communication, accounting, office expenses, and the Operator's share of payroll taxes and insurance.

Except for amounts claimed under "fixed unit costs" provisions of the contract, all costs claimed in this voucher must be supported by documentary evidence consisting of: (a) certified copies or transcripts of payrolls which list each employee, wage rate, period of employment, gross earnings, itemized deductions, and net earnings; (b) original or certified copies of invoices, statements of accounts, or purchase orders which indicate items of materials or services, quantities, unit prices, total charges, and payment terms; and (c) certified memoranda of the Operator for such items as depreciation of Operator-owned equipment, unemployment taxes, and employee's liability insurance. The certification may be stated thus, "Certified True Copy (or Transcript)", followed by the signature of the Operator or his agent. One copy of each document should accompany the original of this voucher.

The requirement for submitting documentary evidence of claimed costs may be waived by the OME regional Executive Officer if he determines that it is impracticable for an Operator to submit this material. In any case of waiver of this requirement an "on-site" audit by an OME auditor is mandatory prior to payment of the final Operator's Monthly Voucher.

INT.DUP.,D.C.59- 61579

MME FORM 61
SEPT. 1959

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION

MAR 25 1960
O.M.E.

OPERATOR'S PROGRESS REPORT

For Month of Feb. 1960 — O.M.E. Docket No. 6045 2102

Operator's Name Baltimore Syndicate Ltd. — Contract No. 14-23-090

OPERATION	UNITS	FOR OPERATOR'S USE: UNITS THIS MONTH	UNITS TO DATE	COSTS TO DATE	FOR GOVERNMENT USE: APPROVED UNITS THIS MONTH	APPROVED UNITS TO DATE	APPROVED COSTS TO DATE
Drifting: Drill Sta.	2	0	2	400.00		2	400.00
Crosscutting							
Raising: Mobil & Demob	1	0	1	150.00		1	150.00
Shafts							
Winzes							
Other Underground							
Drilling, Core-Diamond	ft.	200	1200	6120.00	200	1200	6,120.00
Rotary: Incid. allow.	ft.	280	280	200.00	200	1200	1200.00
Drilling, Non-core-Diamond	ft.						
Rotary: Overreaming	ft.	80	80	240.00	72	72	180.00
Churn							
Percussion							
Miscellaneous: Core boxes	ea.	5	28	112.00	5	28	112.00
Roads and Trails							
Stripping							
Trenching							
Test Pitting							
Other Surface Work							
Initial Rehabilitation and Repairs							
Rehabilitation of Mine Workings: Hope tunnel				750.00			750.00
New Buildings, Fixtures, etc.							
Operating Equipment Purchases							
Analytical Work: 16 assay determination				27.00			22.00
TOTAL TO DATE (per MME Form 60)				8999.00			8934.00

REMARKS

Diamond drilling is completed as faras stage one is concerned. As soon as your geologist can come over, we can go over the Cores and examine and log them, also go over any other data, in preparation for stage two.

(Continue on back)

REMARKS

(Continue on back)

The undersigned company, and the official executing this certification on its behalf, hereby certify that the information contained in this report is correct and complete to the best of their knowledge and belief.

Date Mar/2/60 Operator Baltimore Syn. Ltd.

Per C. M. Wagner Title General Partner

A willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction is a criminal offense. (U.S. Code, Title 18, Sec. 1001.)

I certify that the information above is complete and accurate to the best of my knowledge and belief.

Signature Original signed by S. W. Zoldak

Title Government Representative

Date

(INSTRUCTIONS ON REVERSE)

REMARKS *(Cont.)*

REMARKS *(Cont.)*

INSTRUCTIONS FOR PREPARING OPERATOR'S PROGRESS REPORT, MME FORM 61

This report is the second of the three parts of the Operator's Monthly Report. Submit the original and four copies.

The cost for each operation should be the total of all claimed costs attributable to that type of work with two exceptions, namely—operating equipment purchased and analytical work which are stated separately. For example, drifting costs should be the total of all costs chargeable to drifting including supervision, technical services, timbering (if any), etc. Similarly, drilling costs should include the cost of cementing, reaming, core boxes, etc. This procedure of distribution holds whether the contract was written on an actual cost or a unit cost basis, or some combination of the two. Distribute the cost of such general items as supervision, equipment rented, etc. according to relative footages or on some other conventional basis. The item "Initial Rehabilitation and Repairs" covers all rehabilitation and/or repairs other than the rehabilitation of mine workings.

The item titled "Drilling, Non-core Percussion" includes all drilling performed with wagon, jack-hammer, stoper and mounted drills. The several items labelled "Other" are provided to take care of particular exploration operations not specified on this form.

Diamond Drill Log

OME Docket No. 6045

Contract No. 14-23-090-2102

HOLE # 6

DIR South 65° E.

BALTIMORE MINE INCLINATION – 30°

DATE DRILLED	SIZE	REMARKS
Feb 1	BX 8'	30' mineralized
Feb 2		30'–35' monzonite
3		35'–42' brecciated qtz. monz.
"		Broken faulted monz with qtz stringers
" 4		
" 5		62'–67' faulted monz & qtz gouge
" 6		67'–78' faulted red harder, solid monz with mineral streaks
Feb. 8, 9, 10		
Drill moving to 20' and coring Feb 11		
	110'	
	120'	
Feb 12		
	163	
Feb 13	175'	water course approx. 15 to 18 gpm
	200'	monz no mineral

MME FORM 6
REV. 2

6157
46677

UNITED STATES
DEPARTMENT OF THE INTERIOR
Office of the Secretary
Accounting Unit
Washington

ADMINISTRATIVE SUSPENSION STATEMENT

Name and Address of Payee: **Baltimore Syndicate, Ltd.**
P. O. Box 755
Heppner, Oregon

Amount Claimed: for February	Differences (Explained Below)	Amount Approved
1,480.00	60.00	1,420.00
Bu. Voucher No.	Payee's Invoice No.	Period
	14-23-090-2102	February 1960

EXPLANATION

Amount claimed for 80 feet of over reaming	$240.00
Amount allowed as charged on receipt from drilling company - 72 feet @2.50	180.00
Difference	60.00

Amount approved for February voucher	1,420.00
Government participiation - 50 %	710.00
Less amount required to be withheld per letter to you from Mr. Weissenborn dated March 18,1960	100.00
Paid this voucher	610.00

Any reclaim for items deducted must be supported by the original of this statement and submitted to the office shown above.

Suspension made by:

(Sgd) Opal M. Mexulle.

Signature

Assistant Chief, Accounting Unit

Title

RECEIVED
MAR 21 1960
OFFICE OF THE SECRETARY
FISCAL SECTION

MME FORM 6 REFERENCE SLIP

REV. 2-59 OFFICE OF MINERALS EXPLORATION

TO:	DATE	INITIALS
1. 110	1/28	[illegible]
2. ~~Mr. Grimard~~ √ 00		
3.		
4.		
5.		
FROM: VVO	1-28	gad

FOR: Check items for action desired

____ Action ____ Reply for signature of ____

____ Approval ____ Investigate ____ Surname

____ Comment ____ Recommendations ____ Signature

____ Conference ____ Rewrite ____ File

____ Instructions ____ Your information

REMARKS:

MME FORM 60
SEPT. 1959

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION

Docket No. 6045
Contract No. 2102
14-23-090
Contract Amount 22,950.00
Gov't. Participation % 50 $11,405.00
Mineral(s) Cu. Pb. Zn.

JAN 28 1960

OME

OPERATOR'S MONTHLY VOUCHER

For Month of Dec. 1959

Operator's Name Baltimore Syndicate Ltd.
Address P. O. Box 755 Heppner, Oregon

COST CATEGORIES	FOR OPERATOR'S USE: MONTHLY TOTAL	PREVIOUSLY REPORTED	TOTALS TO DATE	FOR GOVERNMENT APPROVAL ONLY: MONTHLY TOTAL	PREVIOUSLY REPORTED	TOTALS TO DATE
Fixed Unit Costs and						
(1) Independent Contracts:						
Drill Site	0	400.00	400.00		400.00	400.00
Rehab. Hope	0	750.00	750.00		750.00	750.00
Grading & Demob.	0	150.00	150.00	150.00	—	150.00
Drilling Core	1417.00	3682.20	5100.00	2040.00	3060.00	5100.00
Incid. Allow.	278.00	722.00	1000.00	400.00	600.00	1000.00
(2) Personal Services:						
Supervision & Technical						
Outside Consultants						
Labor						
(3) Operating Mat'l. & Supplies:						
Timber						
Explosives						
Pipe						
Rail						
Core boxes	36.00	56.00	92.00	36.00	56.00	92.00
(4) Operating Equipment:						
Rental						
Purchase						
Depreciation						
(5) Initial Rehab. & Repairs:						
Buildings, Fixtures, etc.						
Operating Equipment						
(6) New Buildings, Fixtures, etc.						
(7) Miscellaneous:						
Repairs to Equipment						
Analytical Work Assays	0	27.00	27.00		22.00	22.00
Payroll Taxes						
Employee's Liability Ins.						
TOTALS	1731.80	5887.20	7519.00	2626.00	4888.00	7514.00

I certify that the above bill is correct and just and that payment therefor has not been received.

Date 1/11/60 *Payee Baltimore Syndicate Ltd.

Per C. M. Wagner Title General Partner

* When a voucher is signed or receipted in the name of a company or corporation, the name of the person writing the company or corporate name, as well as the capacity in which he signs, must appear. For example: "John Doe Company, per John Smith, Secretary," or "Treasurer," as the case may be.

A willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction is a criminal offense. (U.S. Code, Title 18, Sec. 1001.)

(INSTRUCTIONS ON REVERSE)

Pursuant to authority vested in me, I certify that this account is correct and proper for payment in the amount of:

$ 1313.00

Signature Dorothy F. Long
(Authorized Certifying Officer)

Date 1/22/60 Vou. No. 4

(SEE OTHER SIDE)

MME FORM 61
SEPT. 1959

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION

JAN 28 1960
O.M.E.

OPERATOR'S PROGRESS REPORT

For Month of December

Docket No. 0045

Operator's Name Baltimore Syndicate Ltd.

Contract No. 14-23-0090-2102

OPERATION	UNITS	FOR OPERATOR'S USE: UNITS THIS MONTH	UNITS TO DATE	COSTS TO DATE	FOR GOVERNMENT USE: APPROVED UNITS THIS MONTH	APPROVED UNITS TO DATE	APPROVED COSTS TO DATE
Drifting Drill Sta.	2	0	2	400.00	–	2	400.00
Crosscutting Mobil. Demob.	1	0	1	150.00	1	1	150.00
Raising							
Shafts							
Winzes							
Other Underground							
Drilling, Core-Diamond	Ft.	278	1000.00	5100.00	400 ft.	1000	5100.00
Incld. Rotary Allow.	Ft.	278	1000.00	1000.00	400 ft.	1000	1000.00
Drilling, Non-core-Diamond							
Rotary							
Churn							
Percussion							
Miscellaneous							
Core boxes	Each	9	23	92.00	9	23	92.00
Roads and Trails							
Stripping							
Trenching							
Test Pitting							
Other Surface Work							
Initial Rehabilitation and Repairs							
Rehabilitation of Mine Workings Hope Tunnel				750.00			750.00
New Buildings, Fixtures, etc.							
Operating Equipment Purchases							
Analytical Work 16 Assay Determinations				27.00	22		22.00
TOTAL TO DATE *(per MME Form 60)*				7519.00			7514.00

REMARKS

(Continue on back)

REMARKS

(Continue on back)

The undersigned company, and the official executing this certification on its behalf, hereby certify that the information contained in this report is correct and complete to the best of their knowledge and belief.

Date Jan. 11, 60 Operator Baltimore Syn. Ltd.

Per C. M. Wagner Title General Partner

A willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction is a criminal offense. (U.S. Code, Title 18, Sec. 1001.)

I certify that the information above is complete and accurate to the best of my knowledge and belief.

Signature (s) Stephen W. Zoldak

Title Mining Engr
Government Representative

Date Jan. 21, 1960

(INSTRUCTIONS ON REVERSE)

BALTIMORE M[illegible] E ONE DOCKET NO. 6045 NARRATIVE

Diamond drill hole #4 was completed from 122' to 198' Dec. 9th. From 105' to 129'~~X~~ 10" was in Qtz. Fe Sulphides. at 154'6" there were qtz streaks from there on it was faulty, monzonite.

Hole #5 which is 151'1" from hole #3 was begun on Dec. 15 as it was a 30 degree setting up the drill required some breaking of rock in order to have enough room before starting and together with the Hollidays resulting in slow progress, however it was completed on Dec 31 at 196'. As hole #1was drilled to 205' and hole #2 was drilled to 207' I borrowed 6' from them to bring holes 4 & 5 to 200'. The first 15' was in qtz.and from there to 104' was Monzonite and altered monz. At 104'to 126' was qtz. with some fe. sulphides, from thereon was broken faulted monzonite.

The Contractors immediately started setting up to begin hole #6 the final hole which is a 30 degree and will be the completion of the drill program. They are being plagued with a shortage of water due to freezing temperatures.

DIAMOND DRILL - BALTIMORE MINE

LOG

HOLE #4

Diameter [illegible] INCHES

INCLINATION FLAT

HOLE #5 151.1' from Log #3

DIRECTION SOUTH EAST

INCLINATION = 30°

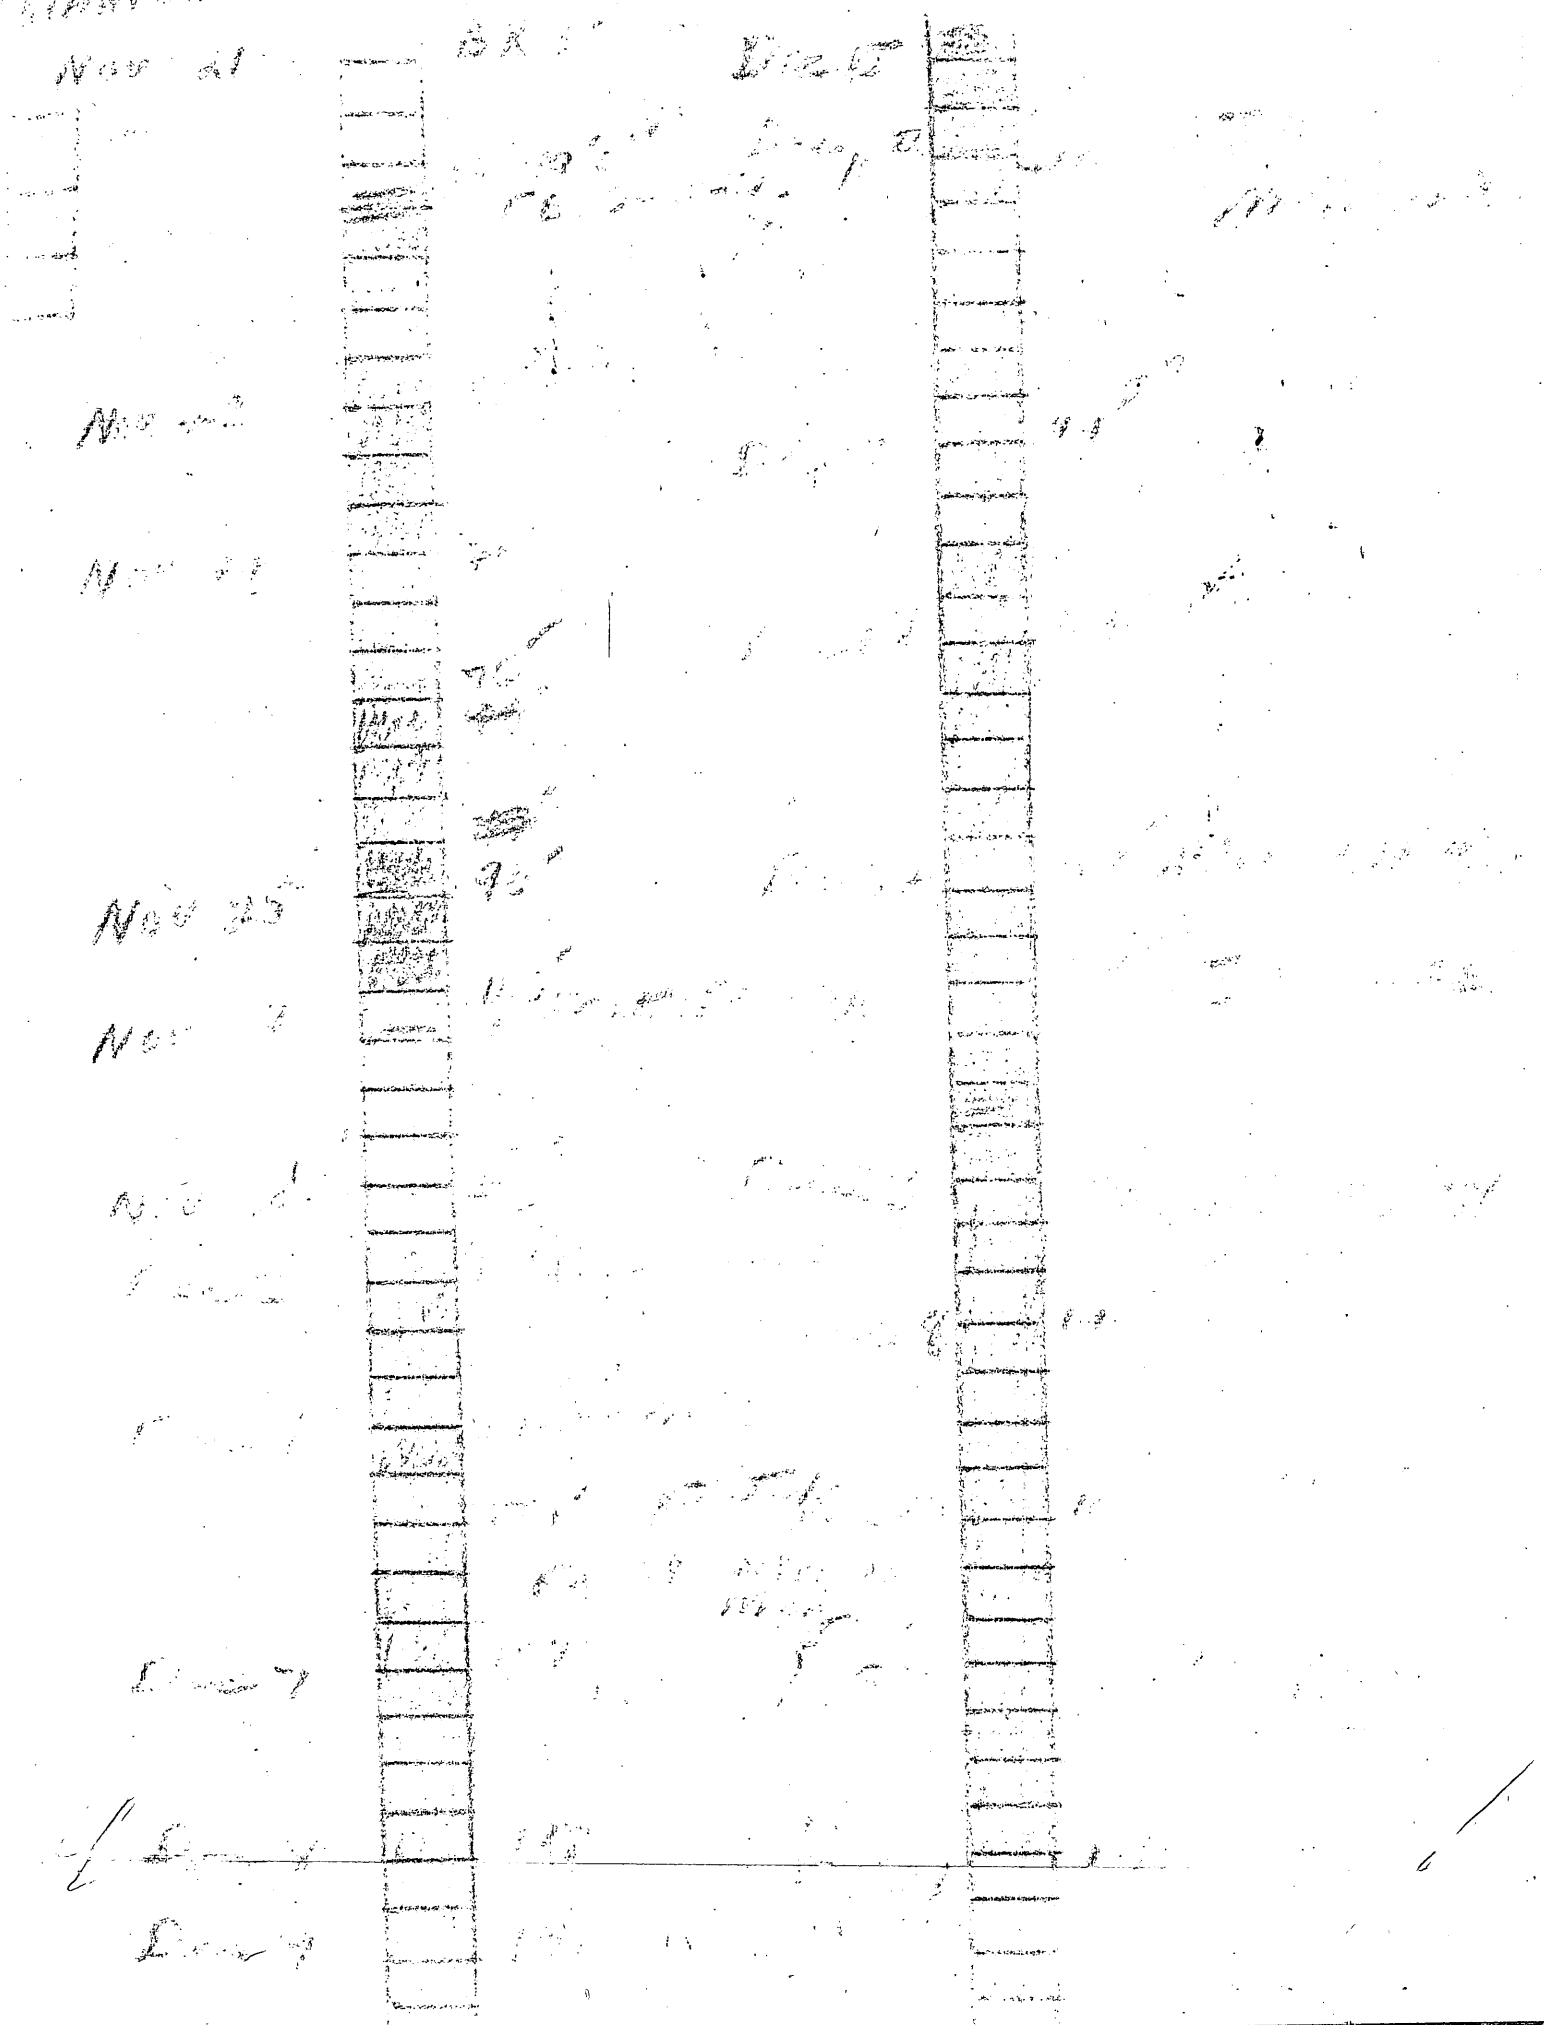

FORM 6 REFERENCE SLIP

R. 12-56 DEFENSE MINERALS EXPLORATION ADMINISTRATION

TO:	INITIALS	DATE
1. 500		
2.		
3.		
4.		
5.		
FROM: 800		

FOR: Check items for action desired

✓ Action	Reply for signature of	
Approval	Investigate	Surname
Comment	Recommendations	Signature
Conference	Rewrite	File
Instructions	Your information	

REMARKS:

Amendment required. Hole No. 1 not at authorized location.

Talbot

1/6/60

INT.-DUP. SEC., WASH., D.C. M25803

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION
So. 157 Howard Street
Spokane 4, Washington
December 14, 1959

OFFICIAL FILE COPY
O. M. E.
RECEIVED DEC 18 1959

DATE	INITIALS	CODE
12-18	gad	NVO
"	[illegible]	110
"	[illegible]	800
12/22	~~Forwarded~~	500

Memorandum

To: Chairman, Operating Committee, OME

From: Executive Officer, OME Field Team, Region I

Subject: Transmittal of inspection report

Enclosed are the original and two copies of the following interim inspection report:

OME		Date
6045	Baltimore Syndicate, Ltd., Baltimore Mine, Jefferson County, Montana	12/10/59

Donald R. MacLaren
Donald R. MacLaren
For: A. E. Weissenborn

Enclosure - in trip.

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION
1201 N. Division St.
Spokane 2, Washington

December 10, 1959

OFFICIAL FILE COPY
O. M. E.
RECEIVED DEC 18 1959

DATE	INITIALS	CODE
12-18	gad	220
		110
12-18	bsr	800
		500

Memorandum

To: OME Field Team, Region I

From: S. W. Zoldok, Mining Engineer, U. S. Bureau of Mines

Subject: Interim inspection report, Docket No. OME-6045 (lead-zinc-copper), Baltimore Syndicate, Ltd., Baltimore Mine, Jefferson County, Montana, Contract No. 14-23-090-2102

The project was inspected on December 2, 1959, accompanied by Mr. Louis Peura, Manager. The previous inspection was made by R. D. Sample, geologist, U. S. Geological Survey, on September 25, 1959.

At the time of the inspection the water supply line was frozen and the drillers never succeeded in thawing the line that day. Freezing will be a continuing difficulty as the mine does not provide enough water for drilling.

The diamond drill station at the 600-foot point consists of a crosscut round taken out on each side of the tunnel. The station at Hole 1 consists of widening out and raising the back of a dog hole crosscut. Both stations comply with contract specifications. It will be necessary to slab off some rock before Holes 5 and 6 can be drilled. This will be done on the Operator's account.

Diamond drill Holes 1, 2 and 3 had been completed and Hole 4 was at 121 feet.

During the inspection it was learned that Hole 1 instead of being drilled from a point about 200 feet from the first station had actually been drilled from the end of the drift (Fig, 1) about 290 feet from the first station. Hole 1, bears S. 45° E., is flat and was stopped at 205 feet. The first 42 feet was in quartz and the balance in quartz-monzonite. The interval from 35.6 to 40.3 feet showed sparse mineralization.

Holes 2, 3 and 4 have been drilled about as shown on Fig. 1, except that no bearings were taken due to the large amount of iron in the drill station. Hole 2 had sparsely mineralized sections from 27.5 to 28.9 feet, 156 to 161.5 feet and 165.3 to 168.0 feet. Hole 3 had a sparsely mineralized section from 21.6 to 26.6 feet and Hole 4 from 17.0 to 20.0 feet.

All diamond drill holes had penetrated sections of barren quartz in addition to the mineralized sections. No detailed log of the core was made. Upon the completion of the diamond drilling all core will be stored at the house of Mr. Louis Peura's Mother in Jefferson City, Montana.

Mr. Louis Peura, manager at the project, had only the contract map as a guide and although the bearing and inclination of Hole 1 are O.K. he was understandably off on the location.

Before leaving the project I spotted inclined Holes 5 and 6 as shown on Fig. 1. This will accomplish the objectives of the exploration.

Status of contract:

Date of contract: July 27, 1959
Termination date: January 27, 1961
Amount of contract: $22,930.00
Amount spent: 3,630.00 (thru Oct. 1959)

Item	Authorized	Completed
Mobilization and Demobilization	$150.00	yes
Diamond drilling	1200 ft.	733'2" 1/
Reaming, casing, etc.	300 ft.	
Core boxes	40	10
Assaying	200 determinations	none
Rehab. Hope Tunnel	$750.00	yes
Repair comp. house	$150.00	no
Incidental allowance	1200 ft.	733'2"
Diamond drill stations	2	2

1/ Hole 1 - 205'
2 - 207'
3 - 200'2"
4 - 121'

S. W. Zoldok

Distribution:
OME (3)
USGS (2)
USBM (AD)
Docket
Zoldok

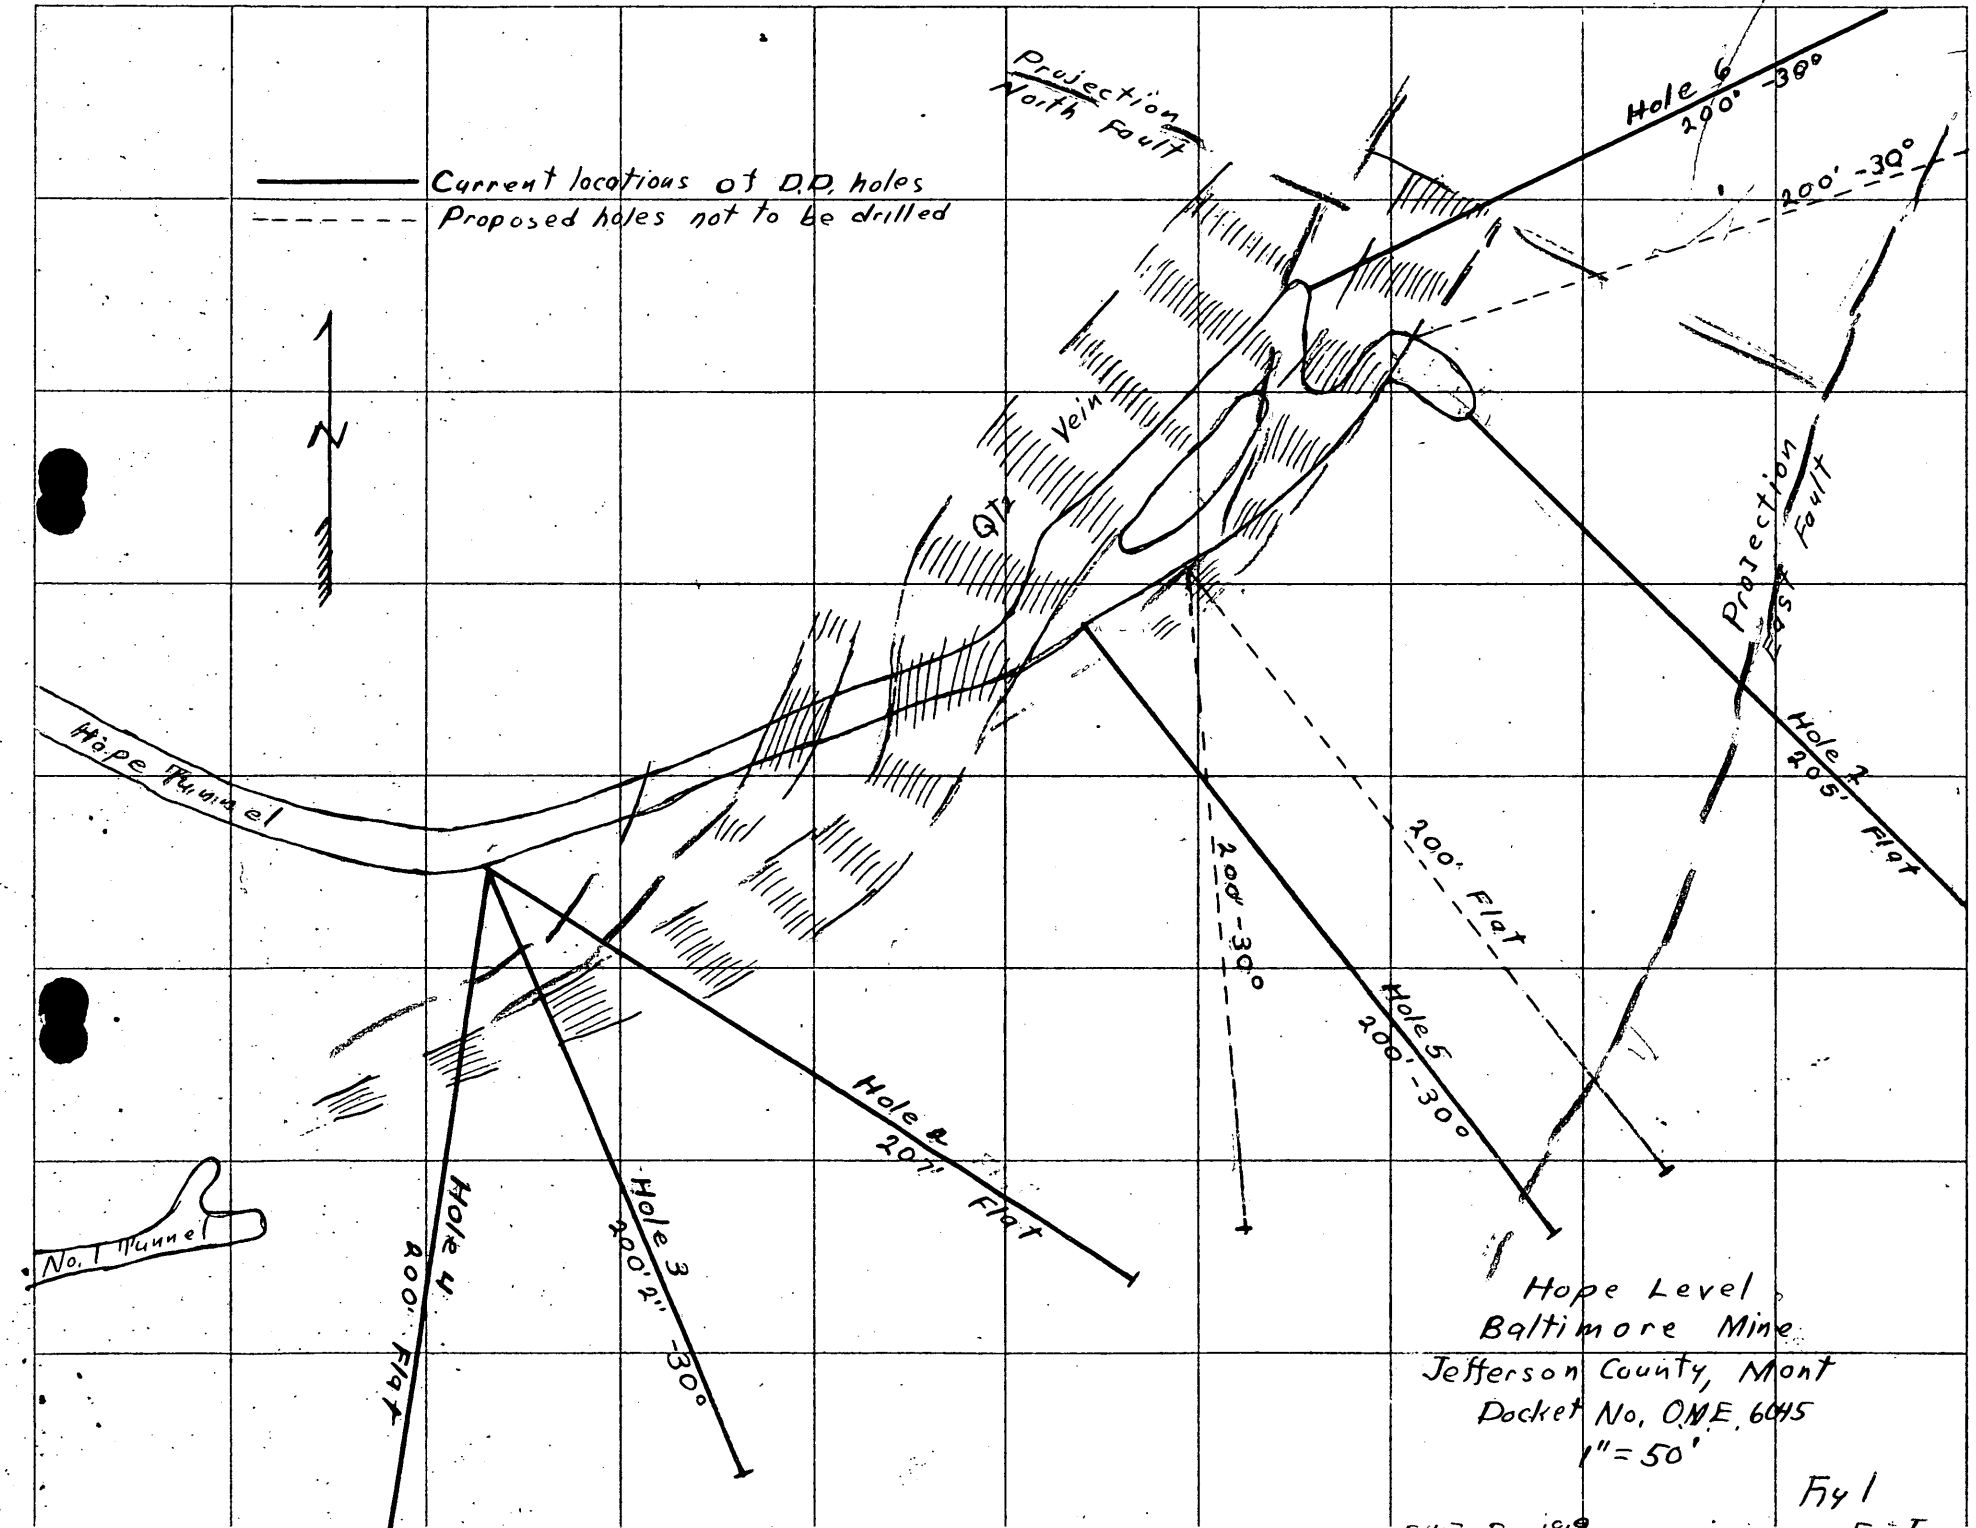

K+E ALBANENE 195M TRACING PAPER 62943
A. Gendron Co., Spokane

OFFICIAL FILE COPY
O. M. E.
RECEIVED DEC 18 1959

DATE	INITIALS	CODE

BALTIMORE MINE OME DOCKET NO. 6045 NARRATIVE

Diamond drill hole #3 was begun on Nov. 3 and completed on Nov. 19. At 22' to 27' Qtz. Fe Sulphides was encountered as it was in hole #2 at 27' to 30'. The balance of the hole was in monzonite except for qtz stringers at 190'. This hole must have been drilled in the fault thereby missing the vein entirely.

On November 2nd I took four samples, two from hole #1 and two from hole #2. Sample #4 hole #2 165'3" to 169' was th e only one that was encourag ing as it showed a mill grade of ore. It was AU. 0.02 AG. 8.8 PB. 0.2 CU. 018.

Hole #4 was commenced on Nov. 21 and at 18' to 20.' encountered the Qtz. Fe. Sulphides again, I took two sludge samples here 18' to 19$ 5"

	AU.	AG.	PB.	CU.
	0.11	4.1	0.2	1.0
19'5" to 20'8"	0.09	3.9		

as the second sample didn't appear to have any color to it I didn't run it for lead and copper, however it would probably have went about the same. At 99' this hole encountered t he Qtz. Fe. Sulphides as far as it was in on Nov. 30. 122'.

The sharp rise in gold indicates this is a new vein and should be prospected by Crosscut and Drifting and perhaps raising.

OME Field Team, Region I

December 17, 1959

OME Certifying Officer, Region I

The Baltimore Syndicate, Ltd., Contract No. 14-83-090-8102
Monthly operating report for November 1959

The subject monthly operating report has been processed and forwarded to the Disbursing Officer for payment.

The difference in the amount claimed and the amount certified for payment is explained as follows:

	Claimed	Approved
322 ft. of diamond drilling claimed, but only 200 ft. was supported by an invoice from the contractor	$1,642.20	$1,000.00
322 ft. incidental allowance	322.00	200.00
Assays - 22 determinations @ $1.00 each	27.00	22.00
	$1,991.20	$1,242.00

The balance of the diamond drilling and incidental allowance will be approved for payment when properly supported by an invoice from the contractor.

Dorothy F. Long

cc: OME (2)
USGS (2)
Contract Admin. & Audit Div. (2)
USBM (AD)

OFFICIAL FILE COPY
O. M. E.
RECEIVED DEC 22 1959

DATE	INITIALS	CODE
12/22	RCW	225
"	KG	110
12/23	[illegible]	500

OFFICIAL FILE COPY
C M E
RECEIVED
DATE

MME FORM 60
SEPT. 1959

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION

DEC 22 1959

Docket No. 6045
Contract No. Q.M.E. 4-23-090 2102
Contract Amount $ 22,930.00
Gov't. Participation % 50 $ 11,465.00
Mineral(s) Cu.Pb. Zn

OPERATOR'S MONTHLY VOUCHER

For Month of Nov. 1959

Operator's Name Baltimore Syndicate Ltd.
Address P. O. Box 755 Heppner, Oregon

COST CATEGORIES	FOR OPERATOR'S USE			FOR GOVERNMENT APPROVAL ONLY		
	MONTHLY TOTAL	PREVIOUSLY REPORTED	TOTALS TO DATE	MONTHLY TOTAL	PREVIOUSLY REPORTED	TOTALS TO DATE
Fixed Unit Costs and						
(1) Independent Contracts:						
Drill Sta.	6	400.00	400.00		400.00	400.00
Bulldozing						
Rehab. Hope	0	750.00	750.00		750.00	750.00
Drifting						
Mobil & Demob.	0	150.00	150.00		—	
Crosscutting						
Drilling Core	1964.20	2440.00	4,404.20	1020.00	2040.00	3060.00
Core						
Incl. allow.				200.00	400.00	600.00
(2) Personal Services:						
Supervision & Technical						
Outside Consultants						
Labor						
(3) Operating Mat'l. & Supplies:						
Timber						
Explosives						
Pipe						
Rail						
Core boxes	16.00	40.00	56.00	16.00	40.00	56.00
(4) Operating Equipment:						
Rental						
Purchase						
Depreciation						
(5) Initial Rehab. & Repairs:						
Buildings, Fixtures, etc.						
Operating Equipment						
(6) New Buildings, Fixtures, etc.						
(7) Miscellaneous:						
Repairs to Equipment						
Analytical Work 16 assays	27.00	0	27.00	22.00	—	22.00
Payroll Taxes						
Employee's Liability Ins.						
TOTALS	2007.20	3,780.00	5,787.20	1258.00	3630.00	4888.00

I certify that the above bill is correct and just and that payment therefor has not been received.

Date Dec. 5, 59 *Payee Baltimore Syndicate Ltd.

Per [signature] M.D. Title General Partner

* When a voucher is signed or receipted in the name of a company or corporation, the name of the person writing the company or corporate name, as well as the capacity in which he signs, must appear. For example: "John Doe Company, per John Smith, Secretary," or "Treasurer," as the case may be.

A willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction is a criminal offense. (U.S. Code, Title 18, Sec. 1001.)

(INSTRUCTIONS ON REVERSE)

Pursuant to authority vested in me, I certify that this account is correct and proper for payment in the amount of:

$ 629.00

Signature [signature]
(Authorized Certifying Officer)

Date 12/17/59 Vou. No. 3

(SEE OTHER SIDE)

Certification by Government Representative:

I certify that to the best of my knowledge and belief the contractor submitting this voucher is operating an exploration project in accordance with the terms of Contract No. 2102

Signature /s/ Stephen W. Zoldok Title Mining Engr. Date 12-14-59

Approved by OME Executive Officer or Alternate:

Signature /s/ A. E. Weissenborn Title Executive Officer Date Dec. 15, 1959

OPERATOR'S MONTHLY REPORT

The Operator, under an Office of Minerals Exploration contract, is required to report monthly to the Government. The report consists of three parts.

FIRST, the Operator's Monthly Voucher on MME Form 60 listing the project costs incurred and claimed by the Operator is the voucher basis for payment of the Government's share of the cost.

SECOND, the Operator's Progress Report on MME Form 61 is a statistical report of the units and cost of of work performed under the contract.

THIRD, the Operator's Narrative Report is a concise description of the work performed, results accomplished, and any unusual situations encountered, illustrated and supported by engineering-geological maps or sketches, drill hole logs, assay reports, etc., as pertinent.

The Operator submits the original and four copies of each of the three sections of this report to the OME regional Executive Officer at the end of each month during the life of the contract.

PREPARATION OF OPERATOR'S MONTHLY VOUCHER, MME FORM 60

After all applicable spaces are filled in, the Operator or his agent must sign the certification in the lower left corner. Categories (2) through (7) apply to "Actual Cost" contracts only.

Under "Fixed Unit Costs" and Category (1) report, (a) the total fixed unit costs of work performed under contract provisions for contribution by the Government on a basis of "fixed unit costs"; and (b) the claimed costs of work performed on a unit-price basis by independent contractors.

Under Category (2) include the claimed costs of all payrolled and invoiced supervisory, technical, and labor personnel, except the costs for services applicable to Categories (5) and (6).

Under Category (3) include the claimed costs of all project materials and supplies other than those used for work under Categories (5) and (6).

Under Category (4) report claimed rentals on equipment belonging to a third party, claimed payments or obligations for payments on the Operator's purchase of equipment, and claimed depreciation for the use of Operator-owned equipment.

Under Categories (5) and (6) include all claimed costs of labor, supervision, technical services, operating materials and supplies, and all other items used in (5) the initial rehabilitation and repairs of existing buildings, fixtures, installations (exclusive of mine workings), and operating equipment; and (6) the installation or construction of new buildings, fixtures, and fixed improvements (exclusive of mine workings). Do not report these costs under Categories (2), (3), (4), and (7).

Under Category (7) include all miscellaneous claimed costs such as repairs (other than initial) and maintenance of equipment, sampling and analysis, travel, communication, accounting, office expenses, and the Operator's share of payroll taxes and insurance.

Except for amounts claimed under "fixed unit costs" provisions of the contract, all costs claimed in this voucher must be supported by documentary evidence consisting of: (a) certified copies or transcripts of payrolls which list each employee, wage rate, period of employment, gross earnings, itemized deductions, and net earnings; (b) original or certified copies of invoices, statements of accounts, or purchase orders which indicate items of materials or services, quantities, unit prices, total charges, and payment terms; and (c) certified memoranda of the Operator for such items as depreciation of Operator-owned equipment, unemployment taxes, and employee's liability insurance. The certification may be stated thus, "Certified True Copy (or Transcript)", followed by the signature of the Operator or his agent. One copy of each document should accompany the original of this voucher.

The requirement for submitting documentary evidence of claimed costs may be waived by the OME regional Executive Officer if he determines that it is impracticable for an Operator to submit this material. In any case of waiver of this requirement an "on-site" audit by an OME auditor is mandatory prior to payment of the final Operator's Monthly Voucher.

MME FORM 61
SEPT. 1959

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION

DEC 22 1959
O.M.E.

OPERATOR'S PROGRESS REPORT

For Month of NOVEMBER 1959 Docket No. 6045

Operator's Name Baltimore Syndicate Ltd. Contract No. 14-23-090-2102

OPERATION	UNITS	FOR OPERATOR'S USE: UNITS THIS MONTH	UNITS TO DATE	COSTS TO DATE	FOR GOVERNMENT USE: APPROVED UNITS THIS MONTH	APPROVED UNITS TO DATE	APPROVED COSTS TO DATE
Drifting Drill Station	2	0	2	400.00		2	400.00
Crosscutting Drill. & Demob	1	0	1	150.00		—	
Raising							
Shafts							
Winzes							
Other Underground							
Drilling, Core-Diamond	ft. 6.10	322	722	4404.20	200	600	3060.00
Rotary Acid, alkali							
Drilling, Non-core-Diamond	ft.				200	600	600.00
Rotary							
Churn							
Percussion							
Miscellaneous							
Roads and Trails Core Boxes	ea. 4.00	4	14	56.00	4	14	56.00
Stripping							
Trenching							
Test Pitting							
Other Surface Work							
Initial Rehabilitation and Repairs							
Rehabilitation of Mine Workings							
New Buildings, Fixtures, etc.				750.00			750.00
Operating Equipment Purchases							
Analytical Work (Return Re assays)				27.00	22		22.00
TOTAL TO DATE (per MME Form 60)				5787.20			4888.00

REMARKS

I am not sure whether I am supposed to carry complete totals ahead or just monthly totals

(Continue on back)

REMARKS

(Continue on back)

The undersigned company, and the official executing this certification on its behalf, hereby certify that the information contained in this report is correct and complete to the best of their knowledge and belief.

Date Dec. 5, 1959 Operator Baltimore Syn. Ltd.

Per C.M. Palmer MD Title General Partner

A willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction is a criminal offense. (U.S. Code, Title 18, Sec. 1001.)

I certify that the information above is complete and accurate to the best of my knowledge and belief.

Signature /s/ Stephen W. Feldok

Title Mining Engr.
Government Representative

Date 12-14-59

(INSTRUCTIONS ON REVERSE)

REMARKS *(Cont.)*

REMARKS *(Cont.)*

INSTRUCTIONS FOR PREPARING OPERATOR'S PROGRESS REPORT, MME FORM 61

This report is the second of the three parts of the Operator's Monthly Report. Submit the original and four copies.

The cost for each operation should be the total of all claimed costs attributable to that type of work with two exceptions, namely—operating equipment purchased and analytical work which are stated separately. For example, drifting costs should be the total of all costs chargeable to drifting including supervision, technical services, timbering (if any), etc. Similarly, drilling costs should include the cost of cementing, reaming, core boxes, etc. This procedure of distribution holds whether the contract was written on an actual cost or a unit cost basis, or some combination of the two. Distribute the cost of such general items as supervision, equipment rented, etc. according to relative footages or on some other conventional basis. The item "Initial Rehabilitation and Repairs" covers all rehabilitation and/or repairs other than the rehabilitation of mine workings.

The item titled "Drilling, Non-core Percussion" includes all drilling performed with wagon, jack-hammer, stoper and mounted drills. The several items labelled "Other" are provided to take care of particular exploration operations not specified on this form.

A. V. TRENT,
Owner-Manager

GOODALL BROTHERS

ASSAYERS AND METALLURGICAL CHEMISTS

46 South Main Street, Helena, Montana

TEL. HI 2-3770
P. O. BOX 537

Date NOV 27 1959

UMPIRE ASSAY _____ CONTROL ASSAY _____ HAND SAMPLE _____

ASSAYED FOR Baldwin Resources Ltd.

MARKS: Box 755, Nyssa, Oregon

Sample No.	DESCRIPTION	GOLD Ozs. Per Ton	SILVER Ozs. Per Ton	WET LEAD Per Cent	COPPER Per Cent	ZINC Per Cent	IRON Per Cent	INSOL. Per Cent	Per Cent	Total Value Per Ton
Drill Hole	18'-19'5"	0.11	4.1	0.2	1.0					7.84
✓	19'5"-20'5"	0.09	3.9							6.66

Gold not determined _____

Charge $ 7.50

GOODALL BROS.

By A. V. Trent

A. V. TRENT,
Owner-Manager

GOODALL BROTHERS

ASSAYERS AND METALLURGICAL CHEMISTS

46 South Main Street, Helena, Montana

TEL. HI 2-3770
P. O. BOX 537

Date Nov 2 - 1959

UMPIRE ASSAY _____ CONTROL ASSAY _____ HAND SAMPLE _____

ASSAYED FOR Baltimore Syndicate Ltd. Dr. C. M. Wagner Box 785 Lyons, Oregon. MARKS:

Sample No.	DESCRIPTION	GOLD Ozs. Per Ton	SILVER Ozs. Per Ton	WET LEAD Per Cent	COPPER Per Cent	ZINC Per Cent	IRON Per Cent	INSOL. Per Cent	Per Cent	Total Value Per Ton
1	Hole 1 35'8" 40'3"	0.005	0.5	0.2	Trace					
2	" 10'6" 15'4"	Trace	0.2	None	Trace					
3	Hole 2 156'5" 161'5"	0.02	0.4	None	Trace					
4	" 165'3" 169'	0.02	8.8	0.2	0.8					

Gold not deducted: _____

Charges $ 20.00

GOODALL BROS.

By A. V. Trent

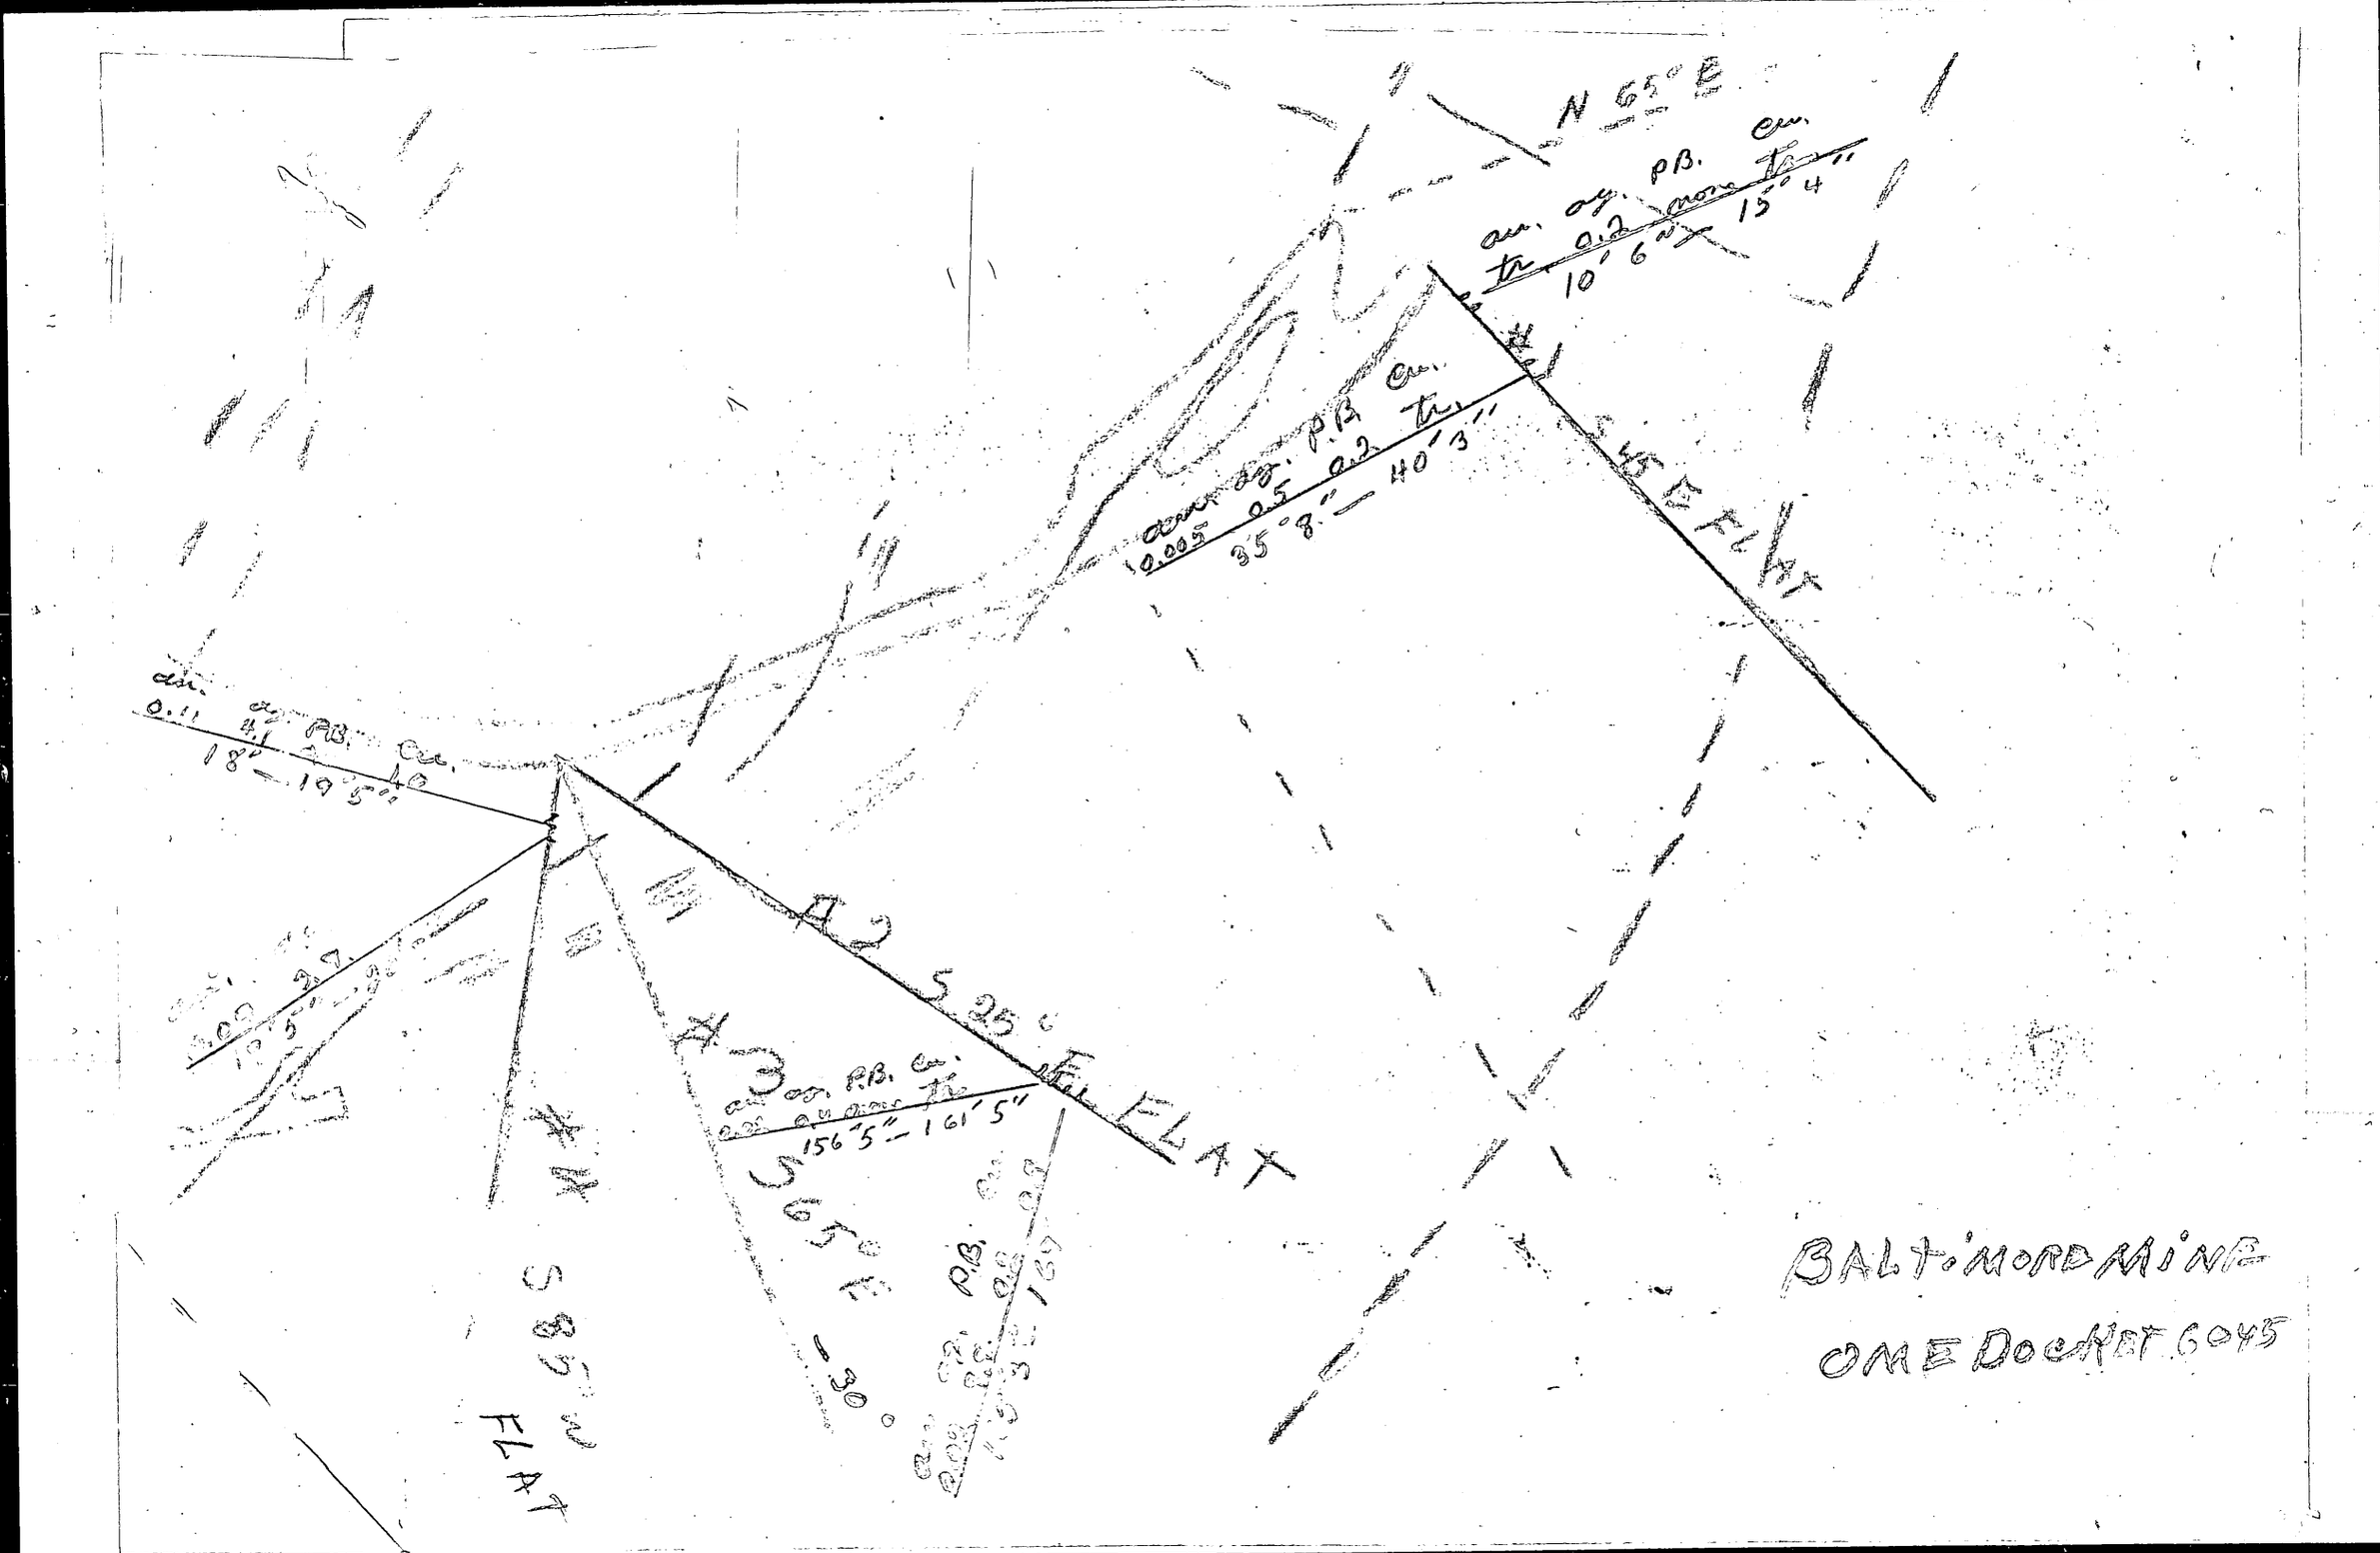
N 65° E
#1 S 45° E FLAT
#2 S 25° E FLAT
#3 S 65° E
#4 S 85° E FLAT
BALTIMORE MINE
OME DOCKET 6045

DIAMOND DRILL LOG BALTIMORE MINE OME DOCKET 6045

Diamond S Eastern Hole # Hole # Surveyed 58% W.

S 85° E

DATE	#	SIZE	REMARKS	DATE	#	SIZE	REMARKS
Monzonite Nov 3		BX		Nov 21		BX	
		AX				AX	
Nov 24		29	3 ore FES-Mnd			18'	ore FE Sulphide
		27				20'	
Nov 5		40'				AX	
		AX					
				Nov 23		50	
Nov 6		70'					
				Nov 24		70'	
Nov							
Nov							
				Monzonite Nov 25		90'	
						92'	
Nov 7		110'					Sig + FE Sulph. Mineralized
				Nov 30		122'	
Nov 9		135'					
Nov 10		153'					
Nov 16		173'	SOFT No Core				
Nov 17		185'	Faulted Mong				
		190'	Stringers				
Nov 18		200'					
Nov 19							

MME FORM 6 REFERENCE SLIP

REV. 8-59 OFFICE OF MINERALS EXPLORATION

TO:		DATE	INITIALS
1.	110	12/14	gg
2. ~~Edward~~	~~FOO~~		
3.			
4.			
5.			
FROM:	NNO	12-14	gad

FOR: Check items for action desired

____ Action ____ Reply for signature of _____

____ Approval ____ Investigate ____ Surname

____ Comment ____ Recommendations ____ Signature

____ Conference ____ Rewrite ____ File

____ Instructions ____ Your information

REMARKS:

MME FORM 60
SEPT. 1959

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION

DEC 1st 1959 O.M.E.

Docket No. 6045
Contract No. 14-23-096 2102
Contract Amount $22,930.00
Gov't. Participation % 50 $ 11,465.00
(Minerals) Lead-Zinc-Copper

OPERATOR'S MONTHLY VOUCHER

For Month of October 1959

Operator's Name Baltimore Syndicate, Ltd.
Address Dr. C. M. Wagner, General Partner
Box 755, Heppner, Oregon

COST CATEGORIES	FOR OPERATOR'S USE: MONTHLY TOTAL	PREVIOUSLY REPORTED	TOTALS TO DATE	FOR GOVERNMENT APPROVAL ONLY: MONTHLY TOTAL	PREVIOUSLY REPORTED	TOTALS TO DATE
Fixed Unit Costs and						
(1) Independent Contracts:						
Mobil. & Demobil.		150.00	150.00			
~~Bulldozing~~						
~~xxxxxx~~ Drill Stations		400.00	400.00		400.00	400.00
Crosscutting						
Drilling (core) 311'	1,618.20	453.90	2,040.00	2040.00	—	2040.00
Inciden. Allowance	311.00	89.00	400.00	400.00	—	400.00
Rehab.-Hope Tunnel		750.00	750.00		750.00	750.00
(2) Personal Services:						
Supervision & Technical						
Outside Consultants						
Labor						
(3) Operating Mat'l. & Supplies:						
Timber						
Explosives						
Pipe						
Rail						
Core boxes 8	32.00	8.00	40.00	40.00	—	40.00
(4) Operating Equipment:						
Rental						
Purchase						
Depreciation						
(5) Initial Rehab. & Repairs:						
Buildings, Fixtures, etc.						
Operating Equipment						
(6) New Buildings, Fixtures, etc.						
(7) Miscellaneous:						
Repairs to Equipment						
Analytical Work						
Payroll Taxes						
Employee's Liability Ins.						
TOTALS	1,951.40	1,850.90	3,760.00	2480.00	1150.00	3630.00

I certify that the above bill is correct and just and that payment therefor has not been received.

Date 11/9/59 *Payee Baltimore Syndicate Ltd.

Per C. M. Wagner Title General Partner

* When a voucher is signed or receipted in the name of a company or corporation, the name of the person writing the company or corporate name, as well as the capacity in which he signs, must appear. For example: "John Doe Company, per John Smith, Secretary," or "Treasurer," as the case may be.

A willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction is a criminal offense. (U.S. Code, Title 18, Sec. 1001.)

(INSTRUCTIONS ON REVERSE)

Pursuant to authority vested in me, I certify that this account is correct and proper for payment in the amount of:

$ 1240.00

Signature Dorothy F. Long
(Authorized Certifying Officer)

Date 12/7/59 Vou. No. 2

(SEE OTHER SIDE)

Certification by Government Representative:

I certify that to the best of my knowledge and belief the contractor submitting this voucher is operating an exploration project in accordance with the terms of Contract No. 2102

Signature /s/ Stephen W. Foldok Title Mining Eng. Date 11-27-59

Approved by OME Executive Officer or Alternate:

Signature /s/ A. B. Weissenborn Title Exec. Officer Date Nov. 30, 1959

OPERATOR'S MONTHLY REPORT

The Operator, under an Office of Minerals Exploration contract, is required to report monthly to the Government. The report consists of three parts.

FIRST, the Operator's Monthly Voucher on MME Form 60 listing the project costs incurred and claimed by the Operator is the voucher basis for payment of the Government's share of the cost.

SECOND, the Operator's Progress Report on MME Form 61 is a statistical report of the units and cost of of work performed under the contract.

THIRD, the Operator's Narrative Report is a concise description of the work performed, results accomplished, and any unusual situations encountered, illustrated and supported by engineering-geological maps or sketches, drill hole logs, assay reports, etc., as pertinent.

The Operator submits the original and four copies of each of the three sections of this report to the OME regional Executive Officer at the end of each month during the life of the contract.

PREPARATION OF OPERATOR'S MONTHLY VOUCHER, MME FORM 60

After all applicable spaces are filled in, the Operator or his agent must sign the certification in the lower left corner. Categories (2) through (7) apply to "Actual Cost" contracts only.

Under "Fixed Unit Costs" and Category (1) report, (a) the total fixed unit costs of work performed under contract provisions for contribution by the Government on a basis of "fixed unit costs"; and (b) the claimed costs of work performed on a unit-price basis by independent contractors.

Under Category (2) include the claimed costs of all payrolled and invoiced supervisory, technical, and labor personnel, except the costs for services applicable to Categories (5) and (6).

Under Category (3) include the claimed costs of all project materials and supplies other than those used for work under Categories (5) and (6).

Under Category (4) report claimed rentals on equipment belonging to a third party, claimed payments or obligations for payments on the Operator's purchase of equipment, and claimed depreciation for the use of Operator-owned equipment.

Under Categories (5) and (6) include all claimed costs of labor, supervision, technical services, operating materials and supplies, and all other items used in (5) the initial rehabilitation and repairs of existing buildings, fixtures, installations (exclusive of mine workings), and operating equipment; and (6) the installation or construction of new buildings, fixtures, and fixed improvements (exclusive of mine workings). Do not report these costs under Categories (2), (3), (4), and (7).

Under Category (7) include all miscellaneous claimed costs such as repairs (other than initial) and maintenance of equipment, sampling and analysis, travel, communication, accounting, office expenses, and the Operator's share of payroll taxes and insurance.

Except for amounts claimed under "fixed unit costs" provisions of the contract, all costs claimed in this voucher must be supported by documentary evidence consisting of: (a) certified copies or transcripts of payrolls which list each employee, wage rate, period of employment, gross earnings, itemized deductions, and net earnings; (b) original or certified copies of invoices, statements of accounts, or purchase orders which indicate items of materials or services, quantities, unit prices, total charges, and payment terms; and (c) certified memoranda of the Operator for such items as depreciation of Operator-owned equipment, unemployment taxes, and employee's liability insurance. The certification may be stated thus, "Certified True Copy (or Transcript)", followed by the signature of the Operator or his agent. One copy of each document should accompany the original of this voucher.

The requirement for submitting documentary evidence of claimed costs may be waived by the OME regional Executive Officer if he determines that it is impracticable for an Operator to submit this material. In any case of waiver of this requirement an "on-site" audit by an OME auditor is mandatory prior to payment of the final Operator's Monthly Voucher.

INT.DUP.,D.C.59- 61579

MME FORM 61
SEPT. 1959

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION

DEC 14 1959 O.M.E.

OPERATOR'S PROGRESS REPORT

For Month of October 1959 Docket No. 6045

Operator's Name Baltimore Syndicate, Ltd. Contract No. 14-23-090- 2102

OPERATION	UNITS	FOR OPERATOR'S USE: UNITS THIS MONTH	UNITS TO DATE	COSTS TO DATE	FOR GOVERNMENT USE: APPROVED UNITS THIS MONTH	APPROVED UNITS TO DATE	APPROVED COSTS TO DATE
Drifting							
Crosscutting							
Raising							
Shafts							
~~Winzes~~ Mobil. & Demob.	Job			150.00			
Other Underground							
Drilling, Core-Diamond	Ft.	311	400	2,040.00	400	400	2040.00
Incid. Allow. Rotary	Ft.	311	400	400.00	400	400	400.00
Drilling, Non-core-Diamond							
Rotary							
Churn							
Percussion							
Miscellaneous							
Drill Stations	Ea.		2	400.00		2	400.00
Roads and Trails							
Stripping							
Trenching							
Test Pitting							
Other Surface Work							
Initial Rehabilitation and Repairs							
Rehabilitation of Mine Workings (Hope Tunnel)				750.00			750.00
New Buildings, Fixtures, etc.							
Operating Equipment Purchases - Core Boxes	10			40.00			40.00
Analytical Work							
TOTAL TO DATE *(per MME Form 60)*				3,780.00			3630.00

REMARKS

(Continue on back)

REMARKS

(Continue on back)

The undersigned company, and the official executing this certification on its behalf, hereby certify that the information contained in this report is correct and complete to the best of their knowledge and belief.

Date 11/9/59 Operator Baltimore Syndicate Ltd.

Per C.M. Wagner Title General Partner

A willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction is a criminal offense. (U.S. Code, Title 18, Sec. 1001.)

I certify that the information above is complete and accurate to the best of my knowledge and belief.

Signature /s/ Stephen W. Zoldok

Title Mining Engr.
Government Representative

Date Nov 27, 1959

(INSTRUCTIONS ON REVERSE)

REMARKS *(Cont.)*

REMARKS *(Cont.)*

INSTRUCTIONS FOR PREPARING OPERATOR'S PROGRESS REPORT, MME FORM 61

This report is the second of the three parts of the Operator's Monthly Report. Submit the original and four copies.

The cost for each operation should be the total of all claimed costs attributable to that type of work with two exceptions, namely—operating equipment purchased and analytical work which are stated separately. For example, drifting costs should be the total of all costs chargeable to drifting including supervision, technical services, timbering (if any), etc. Similarly, drilling costs should include the cost of cementing, reaming, core boxes, etc. This procedure of distribution holds whether the contract was written on an actual cost or a unit cost basis, or some combination of the two. Distribute the cost of such general items as supervision, equipment rented, etc. according to relative footages or on some other conventional basis. The item "Initial Rehabilitation and Repairs" covers all rehabilitation and/or repairs other than the rehabilitation of mine workings.

The item titled "Drilling, Non-core Percussion" includes all drilling performed with wagon, jack-hammer, stoper and mounted drills. The several items labelled "Other" are provided to take care of particular exploration operations not specified on this form.

Baltimore Mine OME Docket No. 6045 Narrative

When D. D. hole no. one was completed, I called Mr. Mc Claren at Ome office Spokane and informed him that this hole cut 42' of Quartz and from thereon it was granitic country rock except for cut ting a fault, I suppose t he East fault, nothing else showed and I recommended not drilling t he 30° down hole at least not in that location to which he and Mr. Sample concurred. So we moved t o no. 2 drill stat ion and st art ed no. two hole in South Easterly direction and H orizont al. At 27' to 30' the Core showed Qtz.z.n. p.b. fe. sulphides, which is encouraging as this is an unexplored area.. We are hopeful the next hole will give more information on this showing. The hole was cont inued to the quartz vein which showed up at 101' to 165' showing qtz. fe. sulphides. from 165' to 207' was monzonite.

Ore Pocket No. 6
Contract No. 14-23-090-2102

DIAMOND DRILL LOG — BALTIMORE MINE

Hole #1 — Direction South of — Inclination Horizontal

Date drilled	Size
SEPT. 15, 1959	3" NX
	2 1/8" BX
	AX
Sept 30 59/89'	
Oct 5, 1959 / 149' talc	FAULT ?
Oct 6 - 169'	
Oct 7 - 186'	
Oct 8 - 205'	

Hole #2 — Direction South of — Inclination Horizontal

Date drilled	Size
Oct 13, 1959	BX
Oct 14	27'
	27' gtz zn 30+ FE Sulfide
	AX
Oct 15	
Oct 16	
Oct 17	
Oct 19	
Oct 20	101' FE+ZN Sulfide
Oct 21	
Oct 22	Sulfide 138'
Oct 23	
Oct 24	149' talc
Oct 26	165' monzonite
Oct 27	
Oct 28	
Oct 29	
Oct 30	207'

D Drill hole # one completed oct 8, 1959
D Drill hole # two " oct 31 1959

Baltimore mine
OMC 6045
Docket #

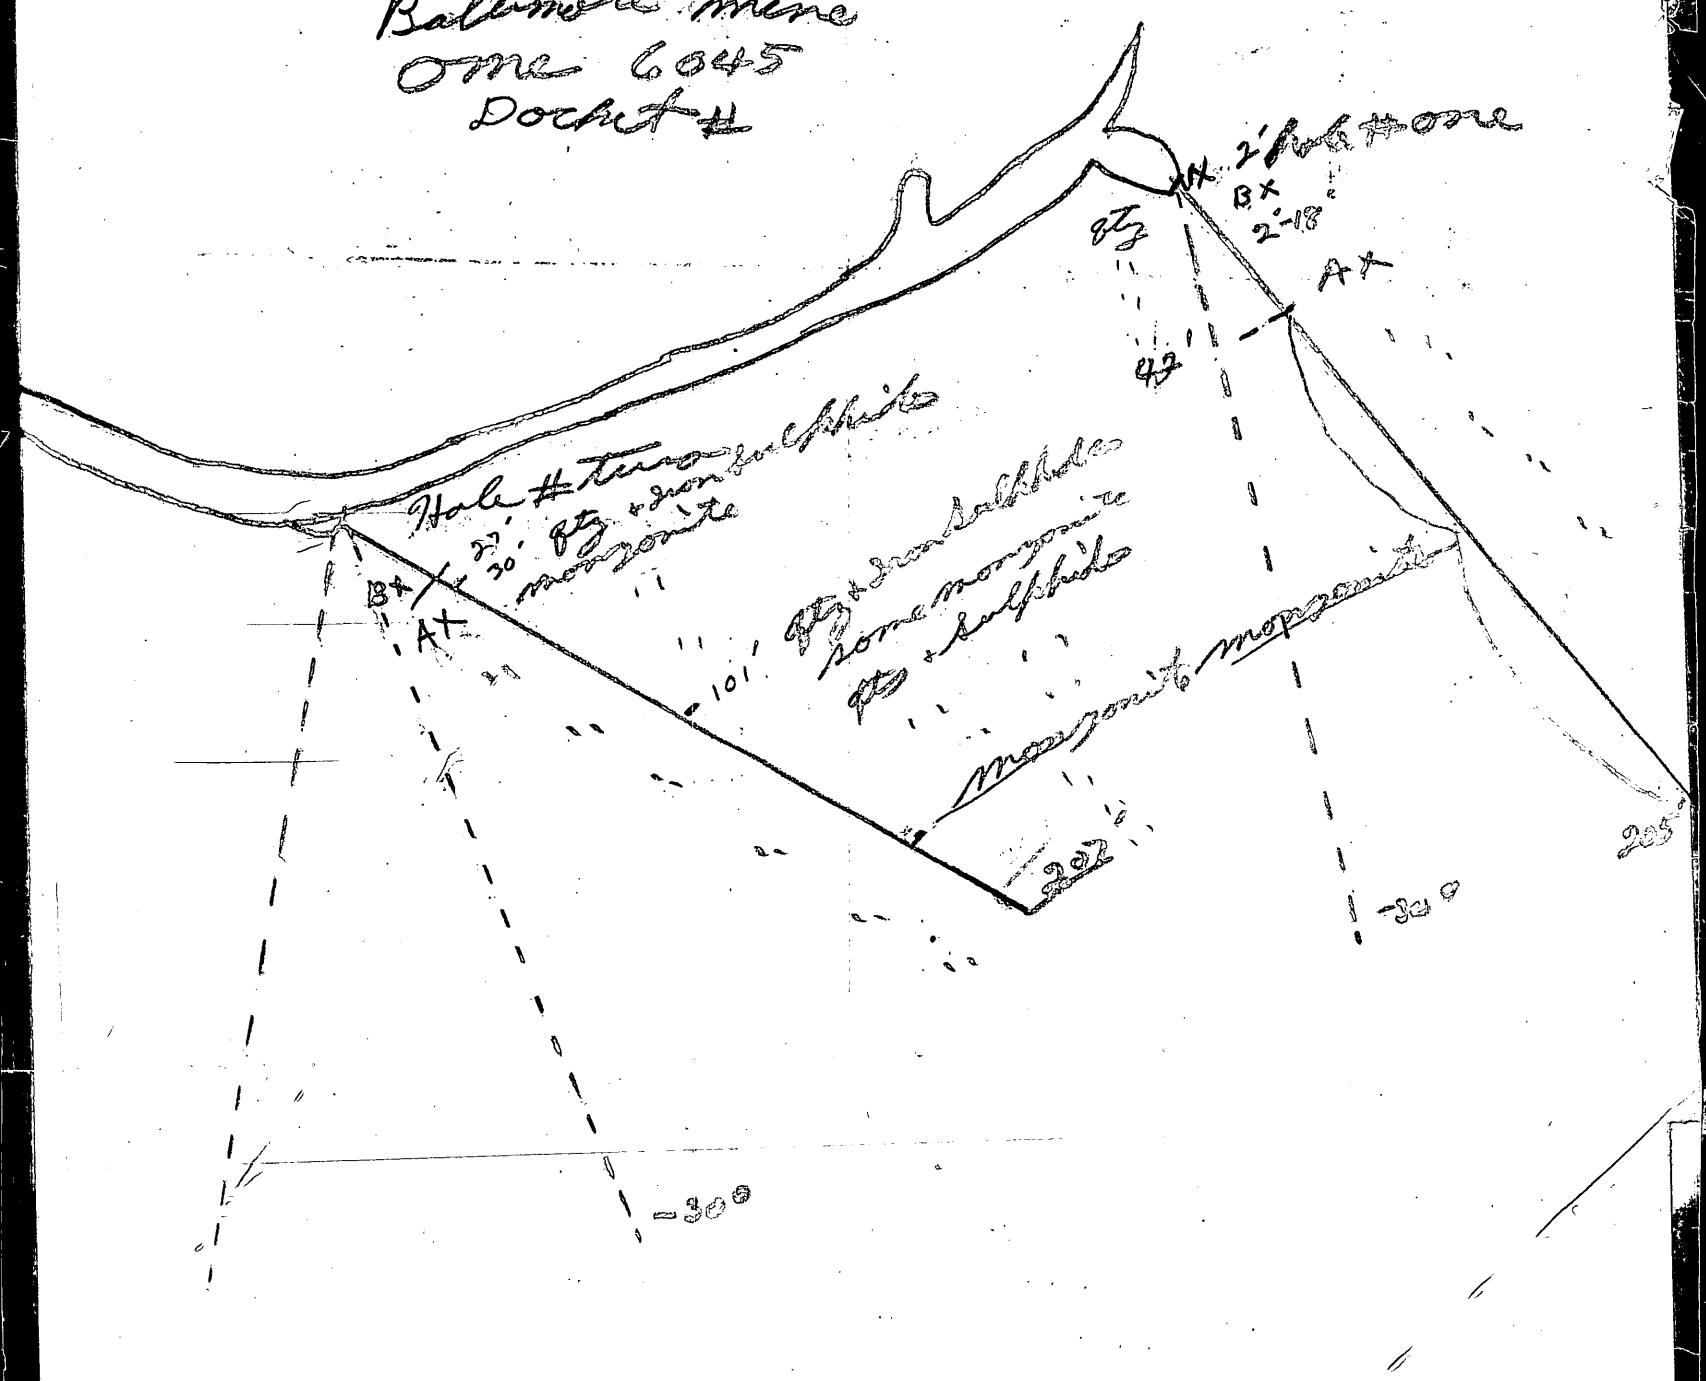

OME Field Team, Region I

December 7, 1959

OME Certifying Officer, Region I

The Baltimore Syndicate, Ltd., Contract No. 14-23-090-2102
Monthly operating report for October 1959

The subject monthly operating report has been processed and forwarded to the Disbursing Officer for payment.

Before we can certify the cost of Mobilization and Demobilization ($150.00) for payment, we must have an invoice from the contractor. Upon receipt of a satisfactory invoice, this item can be approved for payment.

Dorothy F. Long

cc: OME (2)
USGS (2)
Contract Admin. (2)
USBM (AD)
Zoldok

EXTRA COPY
O. M. E
RECEIVED DEC 14 1959

DATE	INITIALS	CODE

DMEA FORM 6 REFERENCE SLIP

REV. 12-56 DEFENSE MINERALS EXPLORATION ADMINISTRATION

TO:	INITIALS	DATE
1. 110	VI/9	[illegible]
2. 500 Mr. Heisendorf		
3.		
4.		
5.		
FROM: 225	RCW	11/9

FOR: Check items for action desired

____ Action ____ Reply for signature of _____

____ Approval ____ Investigate ____ Surname

____ Comment ____ Recommendations ____ Signature

____ Conference ____ Rewrite ____ File

____ Instructions ____ Your information

REMARKS:

OME Field Team, Region I

November 2, 1959

OME Certifying Officer, Region I

6045

The Baltimore Syndicate, Ltd., Contract No. 14-03-090-2102
Monthly operating report for September 1959

The subject monthly operating report has been processed and forwarded to the Disbursing Officer for payment.

The following items have not been certified for payment because they are "Actual Cost" items and must be supported by invoices from the contractor:

Drilling	
Mobilization and demobilization	$150.00
89 ft. of core drilling	453.90
Operating materials and supplies	
2 core boxes	8.00

Pending receipt of invoices covering the drilling, these items, as well as the incidental allowance, will be reinstated.

We have deleted the 800 ft. of pipe in the amount of $400.00, and truck in the amount of $400.00. These items are included in the cost of Rehabilitation of the Hope Tunnel.

Dorothy F. Long

cc: Operator
OME (2)
USGS (2)
Contract Admin. & Audit Div. (2)
USBM (AD)

EXTRA COPY
O. M. E.
RECEIVED NOV 9 1959

DATE	INITIALS	CODE

Form MF-104 (Rev.)
(April 1952)

Budget Bureau No. 42-R1036.5

UNITED STATES
DEPARTMENT OF THE INTERIOR
DEFENSE MINERALS EXPLORATION ADMINISTRATION

NOV 9 1959 O.M.E.

OPERATOR'S MONTHLY REPORT AND VOUCHER

14-23-090

Month of September, 1959 Docket No. DMEA 6045 Contract No. 2102
Operator's Name Baltimore Syndicate, Ltd. Minerals Lead, Zinc, Cu.
Address Dr. C. H. Wagner, Gen. Part. Box 755 Hepnor, Ore.
Contract Amount, $ ~~2050.00~~ 22,930.00 Government Participation: 50% Amount, $ ~~1025.45~~ 11,465.00

ITEMS OF COSTS	FOR OPERATOR'S USE: Monthly Total	Totals Previously Reported	Totals To Date	FOR GOVERNMENT USE ONLY: Approved Monthly Total	Approved Totals Previously Reported	Approved Totals To Date
(1) Independent Short Form Contracts:						
Drilling Core 89'	455.00	none	455.00			
Bulldozing						
Crosscutting						
Drifting						
Mobilization & Demob.	150.00	none	150.00			
(2) Labor and Supervision:						
Labor						
Supervision						
Technical Services						
(3) Operating Mat'ls. and Supplies:						
Timber						
Explosives						
Pipe 2" 800' @ .50	400.00	none	400.00			
Track	400.	"	400.00			
2 core boxes	8.00	none	8.00			
(4) Operating Equipment:						
Rental						
Purchase						
Depreciation						
(5) Initial Rehabilitation and Repairs						
(6) New Bldgs., Improvements, etc.						
(7) Miscellaneous:						
Repairs to Equipment						
Sampling and Analysis						
Payroll Taxes						
Liability Insurance						
Rehab. rope tunnel	750.00	none	750.00	750.00	—	750.00
2 Drill sta. @ 200.00	400.00	none	400.00	400.00	—	400.00
(8) Contingencies (specify):						
Rehab. rope tunnel	750.00	none	750.00			
Incidental allowance	89.00	none	89.00			
Diamond drilling (ft)						
TOTALS	2050.00	none	2050.00	1150.00	—	1150.00

I certify that the above bill is correct and just and that payment therefor has not been received.

Date 10-10-59 *Payee Baltimore Syndicate Ltd

Per [illegible] Title [illegible]

*When a voucher is signed or receipted in the name of a company or corporation, the name of the person writing the company or corporate name, as well as the capacity in which he signs, must appear. For example: "John Doe Company, per John Smith, Secretary," or "Treasurer," as the case may be.

NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

(Instructions on reverse)

Pursuant to authority vested in me, I certify that this account is correct and proper for payment in the amount of:

$ 575.00

Signature Dorothy H. Long
(Authorized Certifying Officer)

Date 11/2/59 Vou. No.
(See other side)

(For Government use only)

CERTIFICATION BY GOVERNMENT REPRESENTATIVE:

I certify that to the best of my knowledge and belief the contractor submitting this voucher is operating a Defense Minerals Exploration Administration project under Contract No. 2102 in accordance with the terms of the contract.

Signature /s/ Stephen W. Zoldok Title Mining Engr. Date 10-19-59

APPROVAL BY ~~DMEA~~ DME EXECUTIVE OFFICER OR ALTERNATE:

Signature /s/ Wing G. Agnew Title Acting Exec. Date 10-28-59

MONTHLY REPORT OF OPERATOR

The Operator (Contractor) of an exploration project is required to make a monthly report to the Government through the Regional Executive Officer. This report consists of three parts as follows:

(a) *Form MF-104—Operator's Monthly Report and Voucher.*—This form details expenditures and constitutes a voucher for reimbursing the Operator for the Government's share of costs;

(b) *Form MF-104A—Operator's Unit Cost and Progress Report.*—This is a statistical report of expenditures which shows costs for the various types of operation; and

(c) *Narrative.*—A concise narrative description of progress made, results accomplished, and any unusual difficulties encountered must be furnished as an attachment to this Report and Voucher. Wherever possible, the narrative is to be illustrated with maps or sketches showing formations penetrated and location and assays of samples taken as well as advances in workings. In the case of diamond drilling or churn drilling, the location and inclination of holes is to be shown on a map; logs and assays also are to be submitted.

The Monthly Report of Operator should be prepared in an original and four copies all of which must be sent to the Executive Officer of the Region not later than the 15th of the month following.

Preparation of Form MF-104—Operator's Monthly Report and Voucher.—All the applicable spaces in Form MF-104 should be filled in by the Operator, and the Operator or his agent should sign the certification in the lower left corner of the form.

The items of costs are arranged in the order they appear in Article 6 (a) of Form MF-200 (Revised February 1952), however, this form is readily adaptable for use in reporting activities under other contract forms.

Under Item (1) delete words "Short Form" if the contract is a sub-contract under Form MF-200; and delete word "Independent" if the contract reported is on Form MF-200 (A). Also, report work paid for on a unit basis under contract Form MF-200 as though it were performed under an independent contract.

Under Item (2) include labor, supervision and technical services incurred for the exploratory operations. Do not include labor, supervision and technical services used for work performed under items (5) and (6).

Under Item (3) include the costs of material and supplies used in the project other than that used under items (5) and (6).

Under Item (4) appear the three types of operating equipment expenditures, that is, rental, purchase and depreciation. The expenditures made for renting equipment belonging to a third party will be reported under "Rental". The amount paid or duly obligated for payment for the purchase of equipment will be reported under "Purchase". The amount of expenditures due the Operator to reimburse him for depreciation of equipment owned will be reported under "Depreciation".

Item (5) comprises costs of labor, supervision, technical services, materials, etc., which are used in the initial rehabilitation and repair of existing buildings, installations, fixtures, and equipment. These costs, therefore, should not be reported under items (2) and (3).

Item (6) includes the labor, supervision, technical services, materials, etc., used in the installation or construction of new buildings, fixed improvements, etc., necessary for the project. These costs, therefore, should not be reported under items (2) and (3).

Item (7) covers miscellaneous types of expenditure such as payroll taxes, liability insurance, workmen's compensation insurance, repairs to equipment and sampling and analysis. Only that part of payroll taxes, liability insurance and workmen's compensation which are paid by the operator should be reported under item (7). The share paid by the employee as a payroll deduction is to be included under item (2) as labor costs.

Item (8) includes any unforeseen costs not included in the other seven categories.

The original of Form MF-104 when submitted for reimbursable expenses incurred under contract Form MF-200 must be supported by original documentation or by certified copies of purchase orders, payrolls or transcripts of payrolls, unless such documentation has been waived by the Regional Executive Officer. This certification may be stated thus, "Certified True Copy (or Transcript)", followed by appropriate signature. If the Executive Officer of the Region determines that a contract under Form MF-200 should have an "on-site" audit, that is, a Government auditor should make an audit of the Operator's books and records of account, the Operator need not support his monthly voucher with original or certified documents except in cases of equipment purchases whose individual costs exceed $50.00. In these cases the original or a certified copy of the purchase order or invoice should be attached to the Monthly Voucher. N. B.—Only the *original* of Form MF-104 is required to be documented. The four copies of Form MF-104 are not to be thus supported.

Form MF-104 submitted for reimbursement under fixed price contracts on Form MF-200 (A), however, are not required to be supported by documentation of any kind. The Operator will submit his claim under item (1) of Form MF-104 by deleting as stated above the word "Independent" and by showing the number of feet or other units immediately after the appropriate descriptive word, such as, drilling, bulldozing, crosscutting, drifting, etc., and giving the "Monthly Total" amount due. "Totals Previously Reported", and "Totals to Date" columns should also be filled in.

Form MF-104A
(April 1952)

Budget Bureau No. 42-R1151
Approval expires 6-30-53.

UNITED STATES
DEPARTMENT OF THE INTERIOR

DEFENSE MINERALS EXPLORATION ADMINISTRATION

OPERATOR'S UNIT COST AND PROGRESS REPORT

Month of [illegible] 195[illegible] Docket No. DMEA [illegible] Contract No. [illegible]
Operator's Name Baltimore Syndicate Ltd. Minerals [illegible]
Address P. O. Box 755 [illegible] Road, [illegible]

OPERATION	Unit	Costs This Month	Units This Month	Costs to Date	Units to Date	Unit Costs to Date	Authorized by Contract: Units	Authorized by Contract: Unit Costs
Drilling: Drill stations	3	600.00	3	600.00	3	200.00	[illegible]	200.00
Crosscutting								
Raising								
Shafts								
Winzes								
Drilling: Core								
Churn	0.10	500.00	00	500.00	000	0.10	1000	0.10
Auger		150.00	1	150.00	1	150.00	1	150.00
Core Discs	0.00	0.00	0	0.00	0	0.00	40	0.00
Stripping								
Trenching								
Test Pits								
Roads and Trails								
Mobilization and D. Rope Reel	1	750.00	2	750.00	1	750.00	1	750.00
Total Distributed Costs		1000.00		1000.00				Total Costs Authorized by Contract
Operating Equipment Purchased								
Initial Rehabilitation and Repairs								
New Buildings, Improvements, etc.								
Pipe and tracks		000.00		000.00				
Total Costs		2650.90		2650.90				

The undersigned company, and the official executing this certification on its behalf, hereby certify that the information contained in this report is correct and complete to the best of their knowledge and belief.

Date 10-10-59 Operator Baltimore Syndicate Ltd.

Per C. M. Haynes M.E. Title Gen Gardner

Remarks:

NOTE.—Title 18, U. S. Code (Crimes), section 1001, makes it a criminal offense to make a willfully false statement or representation to any department or agency of the United States as to any matter within its jurisdiction.

(Instructions on reverse)

(For Government use only)

/s/ Stephen W. Zoldok Mining Engr.

NOV 9 1959 O.M.E.

INSTRUCTIONS

Preparation of Form MF–104A—Operator's Unit Cost and Progress Report.—Applicable places on Form 104A should be filled in by the Operator. The purpose of this form is twofold as follows: (1) to furnish the supervising engineers and other administrators with statistical information necessary to better determine the progress of the project; and (2) to furnish more permanent information on mining costs for future use. The more important phases of operation on which permanent information is desired have been outlined in the form. There are blank lines, however, for those unusual phases which may need to be reported for a particular project. It will be necessary for the Operator to distribute his costs among the applicable phases reported with the exception of three items the costs of which are not to be distributed by the Operator. These three items are: "Operating Equipment Purchased", "Initial Rehabilitation and Repairs", and "New Buildings, Improvements, etc." The reason for not distributing these items on a monthly basis is doubtless clear to the Operator, since such distribution might well overstate the cost for any one month or period short of the entire contract period.

Form MF–104A has been designed to tie in with Form MF–104 for both monthly and cumulative costs. The "Total Costs" on Form MF–104A for each month should equal the monthly "Total Costs" as reported on Form MF–104. This is also true of the "Total Costs To Date".

In preparing Form MF–104A, it will be necessary frequently to distribute certain costs over a number of items. For instance, supervisory and engineering costs may have to be distributed over several phases, such as, drifting, crosscutting, raising, etc., provided that these items were reported active for the month. Such distributions should be made on the basis of time spent on the various phases, on man days of labor charged to such phases, or on some other equitable basis. "Operating Equipment", "Initial Rehabilitation and Repairs", and "New Buildings Improvements, etc.", will be distributed to the several phases of the project by the Washington Office of DMEA at the close of the project if determined necessary. The last two columns headed "Authorized by Contract" will be filled in by the Operator if such information is found in the contract. This information is usually a part of Exhibit "A" of the contract. A space for remarks has been provided for the use of the Operator to call attention to any unusual circumstances causing excessive or disproportionate unit costs.

GPO 83-38475

Monthe of September 1959
Dr. C. M. Wagner
General Partner
The Baltimore Syndicate, Ltd.
P. O. Box 755
Heppner, Oregon

Docket No. OME-6045
Lead, Zinc, Copper

Baltimore Mine
Jefferson County
Montana

Contract No. 14-23-090-2102

NARRATIVE

As soon as the OME contract was received, regabilitation of the Hope tunnel was begun. Rails and pipe was purchased and installed together with cleaning up the rock and debres, then the diamond drill stations were cut, excavation for a new compressor house was done, but the building isn't began as yet, although the compressor is set in the space and is furnighing the necessary air.

Diamond core drilling was began by the contractors F. W. Bell & Gustave Carlson on September 15, 1959 in the right hand face of the Hope tunnel where the first Drill station was cut. Number one hole is horizontal and is being drilled in a Southerly direction , approximately S55E. The first 42' was in Quartz with some mineralization all the way, but from 29' to 42' appears to be somewhat more mineralized. No core has been split and assayed as yet. As of September 30, 1959 the hole has progressed to 89' and appears to be in Monzonite.

Signed Oct 6, 1959 Supervisor Louis Perna

The Baltimore Syndicte, Ltd.

General Partner C M Wagner MD

Hole # 1
direction Southerly S 55° E
inclination Horizontal
Diamond Drilling
began Sept 15, 1959

Sept 30

Hole
Southerly
S 55° E

HOPE TUNNEL

The Baltimore Syndicate
C.M. Wagner M.D. Gen Partner
O.M.E. Docket 6045
Report Period Sept 15 to Sept 30 1959

UNITED STATES
DEPARTMENT OF THE INTERIOR
OFFICE OF MINERALS EXPLORATION
So. 157 Howard Street
Spokane 4, Washington
October 15, 1959

OFFICIAL FILE COPY
O. M. E.
RECEIVED OCT 26 1959

DATE	INITIALS	CODE
10-26	gad	220
"	[illegible]	110
10/27	[illegible]	800
10/27	Friedrich	500

Memorandum

To: OME Field Team, Region I

From: R. D. Sample, Geologist, U. S. Geological Survey

Subject: Initial Inspection Report, Docket No. OME-6045 (Lead-Zinc-Copper), Baltimore Syndicate, Ltd., Baltimore Mine, Jefferson County, Montana, Contract No. 14-23-090-2102

The Baltimore mine was visited and inspected on September 25, 1959. Mr. Louis Peura, Manager, was present and helped with the underground inspection. Two practical miners were finishing the drill site about 600 feet from the portal of the Hope adit. Two diamond drill men were at the drill site about 200 feet beyond where they had been drilling the first flat diamond drill hole to the southeast. However, at the time of visit the drill was idle waiting for a special type of bit to arrive from the factory. The drill hole was started in the very hard iron-stained quartz rib at the face of the drill site. The total advance had been 32.2 feet. Below are the measurements at the time of inspection:

Collar started NX bit	2.0	feet
Drilling with BX bit	16.1	"
Drilling with AX bit	14.1	"
Total	32.2	feet

Rehabilitation of the Hope adit has been completed with track and ore cars. A two-stage, air-cooled, portable compressor sits near the portal entrance and furnishes air for the mining and drilling. No housing has yet been placed around the compressor, but plans are made to do so before the heavy snows. It will also be used for a change room.

Water for operations is pumped from a small reservoir on the creek floor.

Distribution:
OME(4) Docket
USBM(2) Sample
USBM(AD)

R. D. Sample
